



Defect Listing

Pipe Segment Refere... A21-5_A21-4	City Oliver Springs	Street Strutt St	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A21-5	Total Length 2	Year Laid	Shape Circular	Location Details	
DS Manhole A21-4	Length surveyed 2	Year Renewed	Height 8	Width 8	Pipe Joint... 4

SPR 9	MPR N/A	PO Number 4397-03	Customer GRW
SPRI 3	MPRI N/A	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR 5122	QMR N/A		
OPR 9	Surveyed By Barry Rogers	Direction Upstream	Date 20150804
OPRI 3	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 07:36
	Date Cleaned 20150804	End Time 07:43	Weather Dry
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A21-4									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
0.0 ft.	Joint Offset Large				0	<input type="checkbox"/>			2
2.0 ft.	Joint Offset Large				0	<input type="checkbox"/>			2
2.0 ft.	Hole Soil Visible				0	<input type="checkbox"/>	12	12	5
2.0 ft.	Survey Abandoned				0	<input type="checkbox"/>			
Remarks: JOINT SEPARATED									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A21-5_A21-4	Oliver Springs	Strutt St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A21-5	2		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A21-4	2		8	8	4




Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A21-4



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

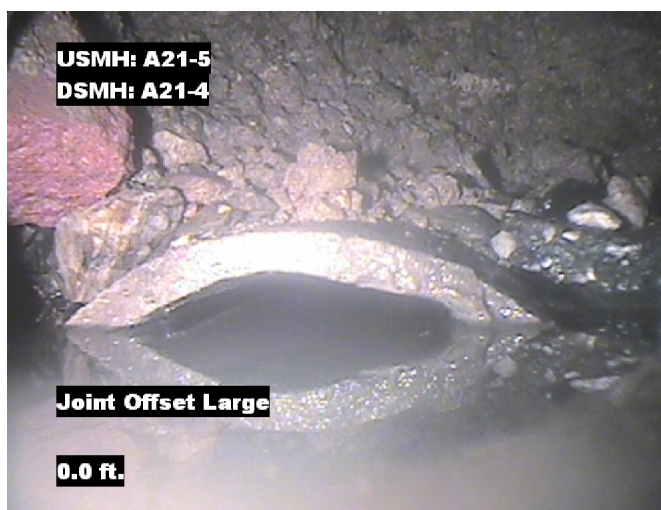

Distance: 0.0 ft. Grade: 2
Condition: Joint Offset Large
Remarks: N/A

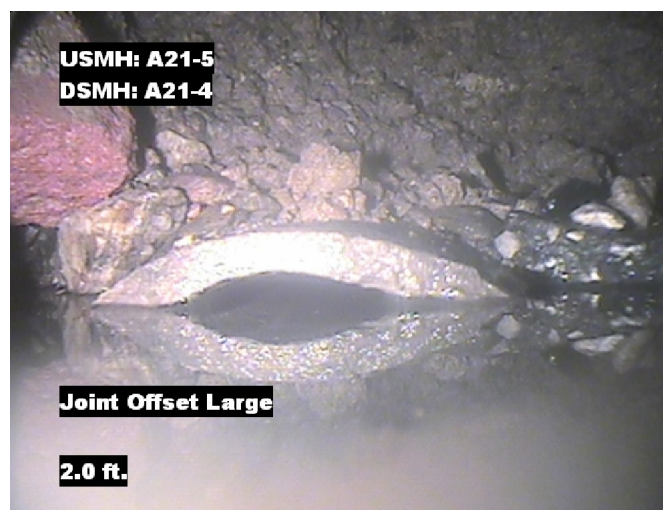


Distance: 2.0 ft. Grade: 2
Condition: Joint Offset Large
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A21-5_A21-4	Oliver Springs	Strutt St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A21-5	2		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A21-4	2		8	8	4

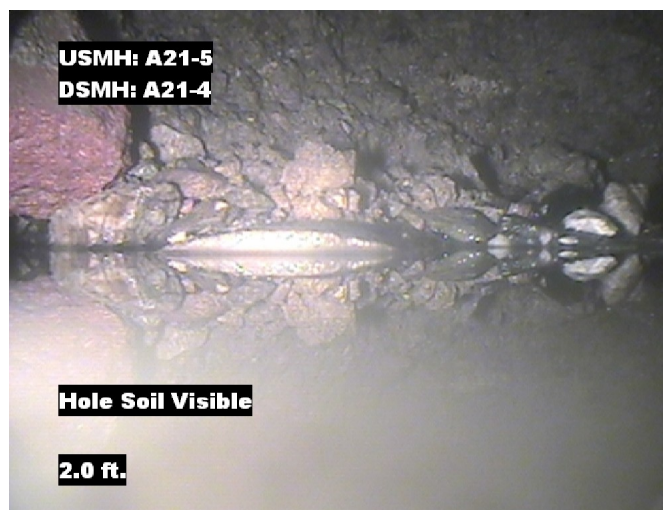

Distance: 2.0 ft. Grade: 5
Condition: Hole Soil Visible
Remarks: N/A

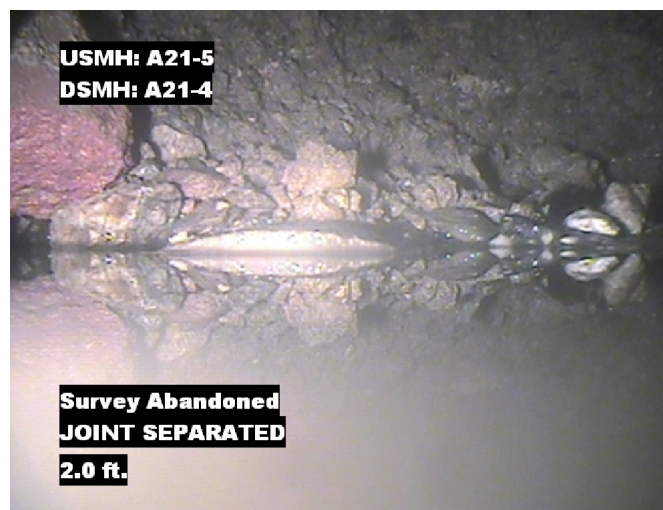

Distance: 2.0 ft. Grade: 0
Condition: Survey Abandoned
Remarks: JOINT SEPARATED



Pipe Segment Refere... A21-5_A21-4	City Oliver Springs	Street Strutt St	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A21-5	Total Length 2	Year Laid	Shape Circular		Location Details	
DS Manhole A21-4	Length surveyed 2	Year Renewed	Height 8	Width 8	Pipe Joint... 4	
SPR 9	MPR N/A	PO Number 4397-03		Customer GRW		
SPRI 3	MPRI N/A	Work Order 4397-02		Purpose		
QSR 5122	QMR N/A			Pre-Rehabilitation Survey		
OPR 9	Surveyed By Barry_Rogers	Direction Upstream	Date 20150804		Media label	
OPRI 3	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 07:36		Weather Dry	
Date Cleaned 20150804			End Time 07:43		Additional Info	

Page #: 4
