



Defect Listing

Pipe Segment Refere... A24-4_A24-3	City Oliver Springs	Street Morgen ST	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A24-4	Total Length 149.8	Year Laid	Shape Circular	Location Details	
DS Manhole A24-3	Length surveyed 149.8	Year Renewed	Height 8	Width 8	Pipe Joint... 4


SPR N/A	MPR N/A	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI N/A	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR N/A		
OPR N/A	Surveyed By Barry Rogers	Direction Downstream	Date 20150803
OPRI N/A	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 06:56
	Date Cleaned 20150803	End Time 07:18	Weather Damp
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A24-4									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
4.5 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
43.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
147.7 ft.	Water Level				5	<input type="checkbox"/>			
149.8 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A24-3									




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A24-4_A24-3	Oliver Springs	Morgen ST	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A24-4	Total Length 149.8	Year Laid	Shape Circular	Location Details	
DS Manhole A24-3	Length surveyed 149.8	Year Renewed	Height 8	Width 8	Pipe Joint... 4

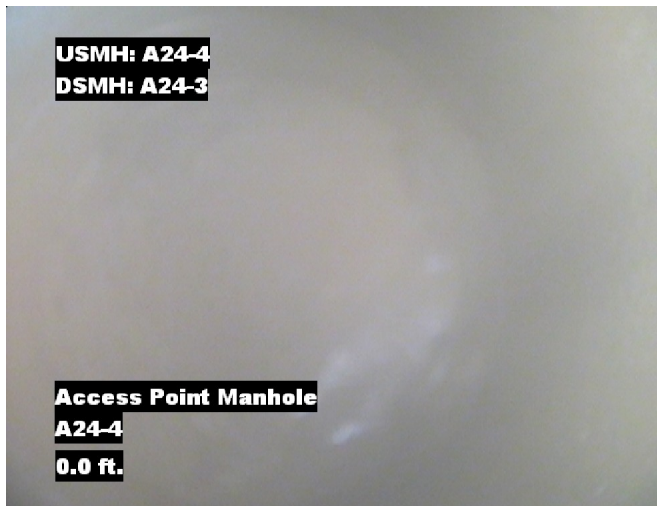


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A24-4

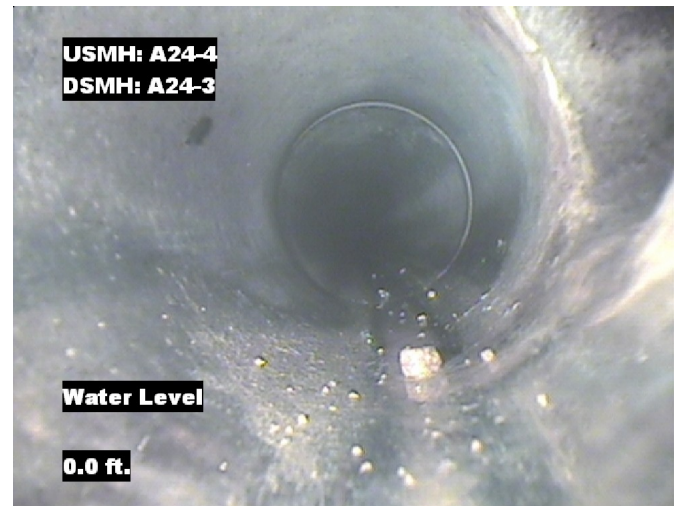

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 4.5 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

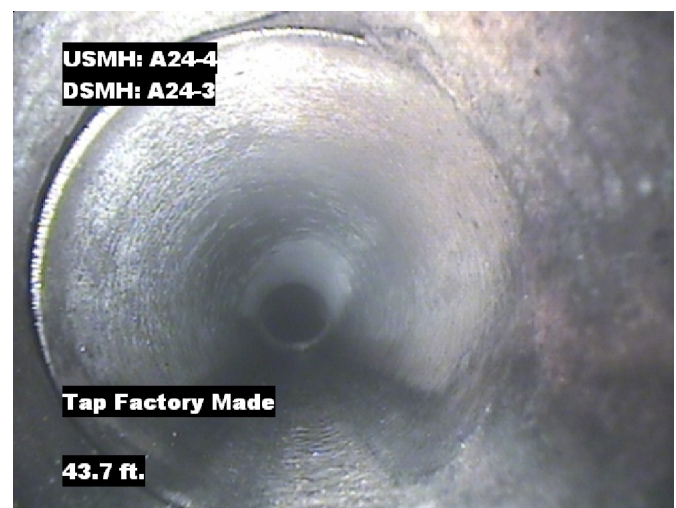


Distance: 43.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere... A24-4_A24-3	City Oliver Springs	Street Morgen ST	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A24-4	Total Length 149.8	Year Laid	Shape Circular		Location Details	
DS Manhole A24-3	Length surveyed 149.8	Year Renewed	Height 8	Width 8	Pipe Joint...	

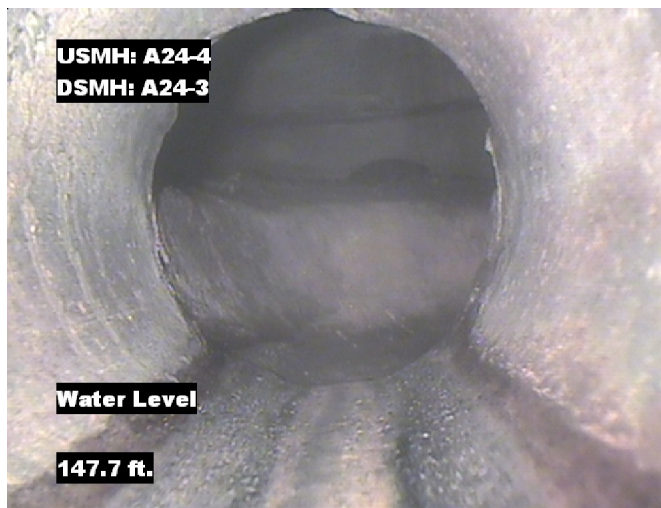

Distance: 147.7 ft. Grade: 0
Condition: Water Level
Remarks: N/A

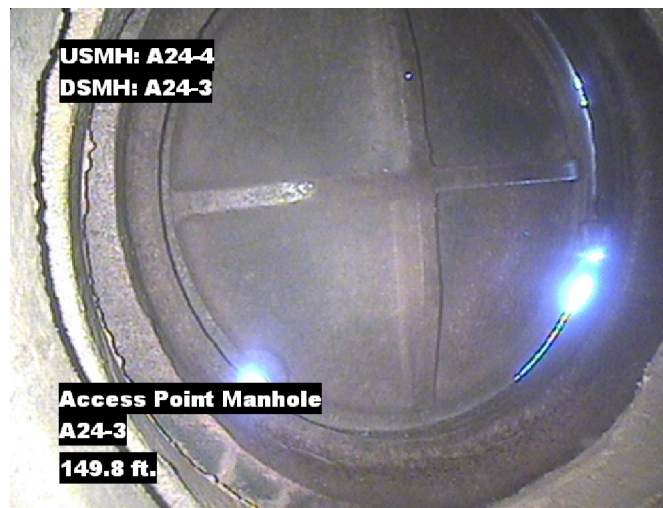

Distance: 149.8 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A24-3



PACP Conditions

Pipe Segment Refere... A24-4_A24-3	City Oliver Springs	Street Morgen ST	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A24-4	Total Length 149.8	Year Laid	Shape Circular	Location Details	
DS Manhole A24-3	Length surveyed 149.8	Year Renewed	Height 8	Width 8	Pipe Joint... 4
SPR N/A	MPR N/A	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI N/A	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR N/A	Direction Downstream		Date 20150803	
OPR N/A	Surveyed By Barry Rogers	Pre-Cleaning Jetting		Media label	
OPRI N/A	Certificate Number U-1012-16405	Time 06:56		Weather Damp	
Date Cleaned 20150803			End Time 07:18		Additional Info

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Code	ID	Length									
