



Defect Listing

Pipe Segment Refere... A27-1_A20-2	City Oliver Springs	Street Springs St	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A27-1	Total Length 250.7	Year Laid	Shape Circular	Location Details	
DS Manhole A20-2	Length surveyed 250.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4


SPR N/A	MPR 10	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 3.3	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 4221		
OPR 10	Surveyed By Charlie Gordon	Direction Downstream	Date 20150825
OPRI 3.3	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 13:13
	Date Cleaned 20150825	End Time 13:28	Weather Dry
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A27-1									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
2.0 ft.	Infiltration Runner				0	<input checked="" type="checkbox"/>	2		4
2.0 ft.	Infiltration Runner				0	<input checked="" type="checkbox"/>	9		4
21.3 ft.	Tap Factory Made Active		8		0	<input type="checkbox"/>	9		
60.0 ft.	Water Level Sag				10	<input type="checkbox"/>			2
88.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
180.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
246.2 ft.	Water Level				10	<input type="checkbox"/>			
250.7 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A20-2									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A27-1_A20-2	Oliver Springs	Springs St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A27-1	Total Length 250.7	Year Laid	Shape Circular	Location Details	
DS Manhole A20-2	Length surveyed 250.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4

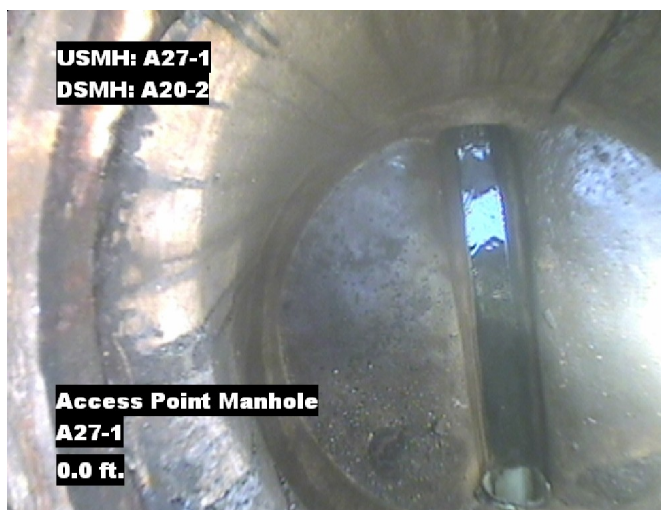


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A27-1



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

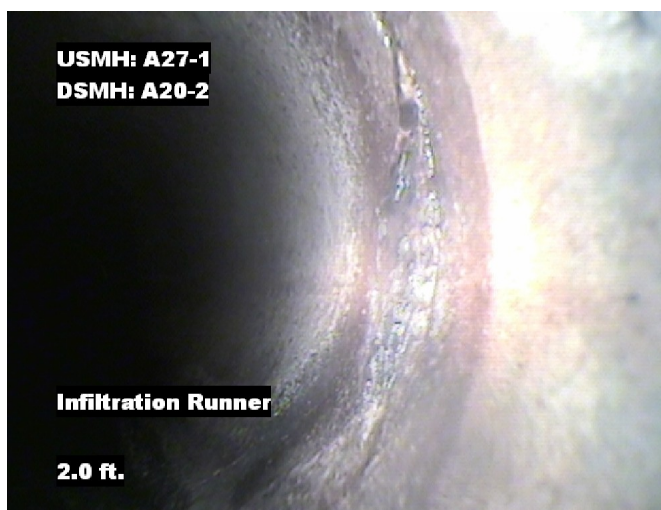

Distance: 2.0 ft. Grade: 4
Condition: Infiltration Runner
Remarks: N/A

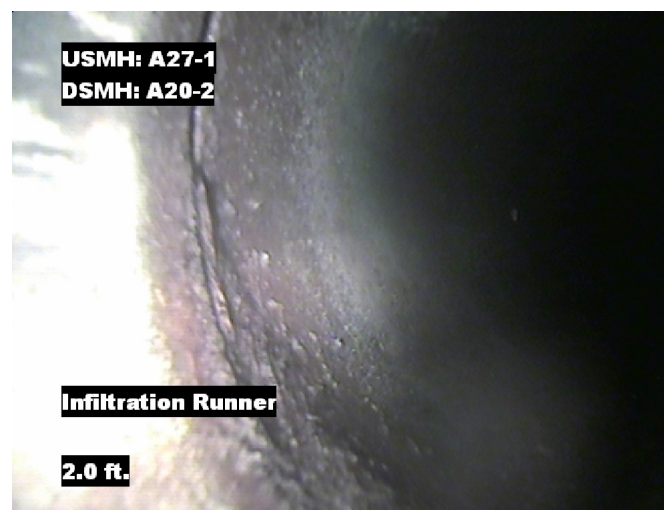

Distance: 2.0 ft. Grade: 4
Condition: Infiltration Runner
Remarks: N/A



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A27-1_A20-2	Oliver Springs	Springs St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A27-1	Total Length 250.7	Year Laid	Shape Circular	Location Details	
DS Manhole A20-2	Length surveyed 250.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4




Distance: 21.3 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A



Distance: 60.0 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A

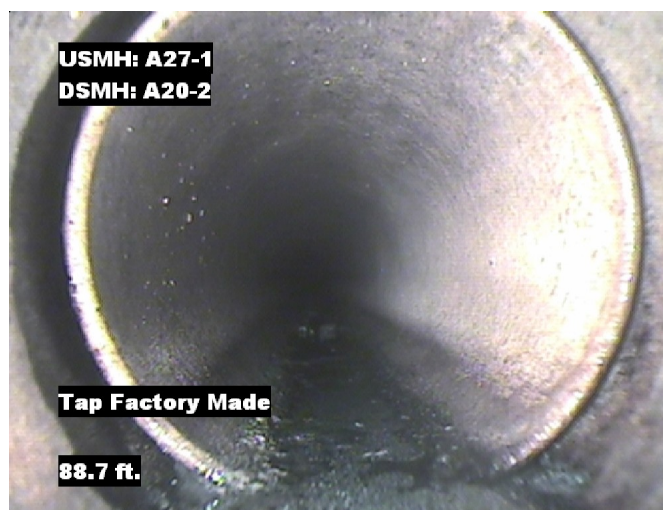

Distance: 88.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

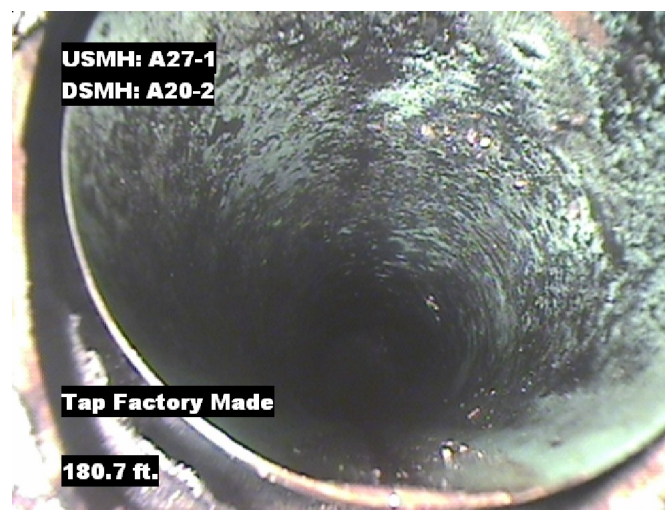

Distance: 180.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere... A27-1_A20-2	City Oliver Springs	Street Springs St	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A27-1	Total Length 250.7	Year Laid	Shape Circular		Location Details	
DS Manhole A20-2	Length surveyed 250.7	Year Renewed	Height 8	Width 8	Pipe Joint...	4



Distance: 246.2 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 250.7 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A20-2



Pipe Segment Refere... A27-1_A20-2	City Oliver Springs	Street Springs St	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A27-1	Total Length 250.7	Year Laid	Shape Circular		Location Details	
DS Manhole A20-2	Length surveyed 250.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4	
SPR N/A	MPR 10	PO Number 4397-03		Customer GRW		
SPRI N/A	MPRI 3.3	Work Order 4397-02		Purpose		
QSR N/A	QMR 4221			Pre-Rehabilitation Survey		
OPR 10	Surveyed By Charlie Gordon	Direction Downstream	Date 20150825		Media label	
OPRI 3.3	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 13:13		Weather Dry	
Date Cleaned 20150825			End Time 13:28		Additional Info	

Page #: 5
