



Defect Listing

Pipe Segment Refere... A28-3_A28-2	City Oliver Springs	Street Highland Dr	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A28-3	Total Length 278.5	Year Laid	Shape Circular	Location Details	
DS Manhole A28-2	Length surveyed 278.5	Year Renewed	Height 8	Width 8	Pipe Joint... 4


SPR 3	MPR N/A	PO Number 4397-03	Customer GRW
SPRI 3	MPRI N/A	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR 3100	QMR N/A		
OPR 3	Surveyed By Charlie Gordon	Direction Downstream	Date 20150820
OPRI 3	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 14:12
	Date Cleaned 20150820	End Time 14:12	Weather Damp
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A28-3									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
24.9 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
80.3 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
136.1 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
143.8 ft.	Hole				0	<input type="checkbox"/>	8		3
144.8 ft.	Tap Break-In		6		0	<input type="checkbox"/>	9		
191.9 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
273.8 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
277.2 ft.	Tap Factory Made Active		8		0	<input type="checkbox"/>	6		
278.5 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A28-2									




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A28-3_A28-2	Oliver Springs	Highland Dr	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A28-3	Total Length 278.5	Year Laid	Shape Circular	Location Details	
DS Manhole A28-2	Length surveyed 278.5	Year Renewed	Height 8	Width 8	Pipe Joint... 4

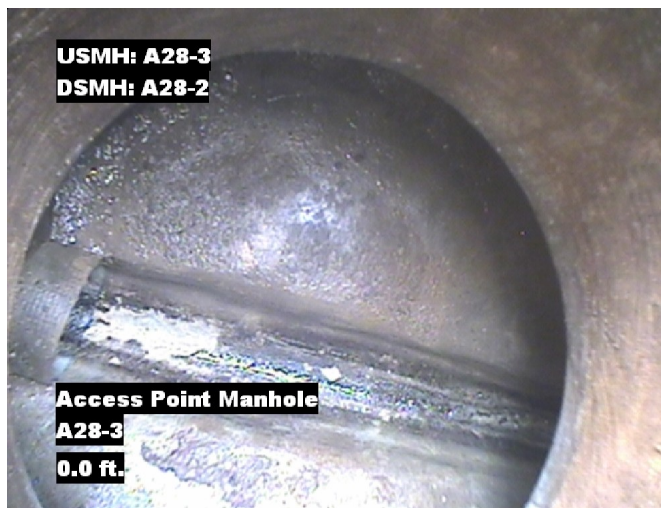


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A28-3

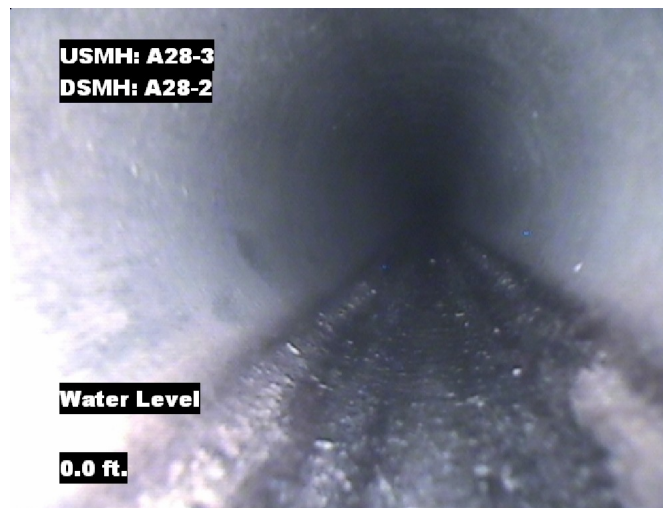

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

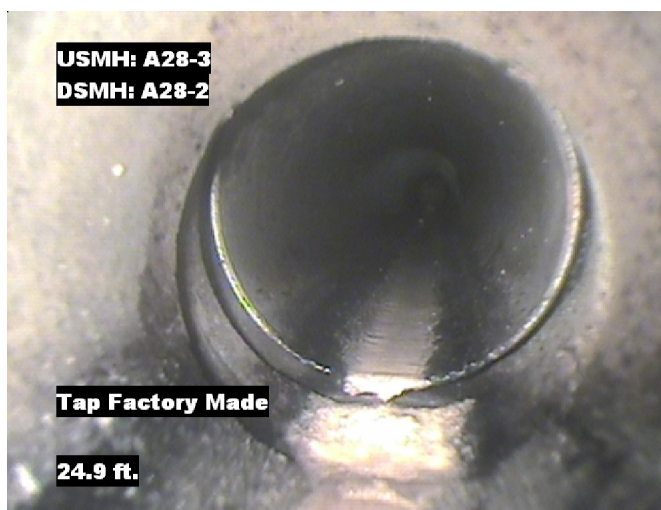

Distance: 24.9 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

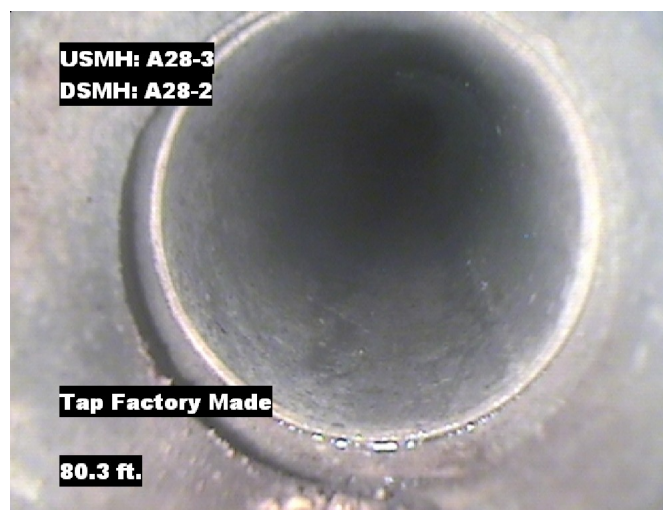

Distance: 80.3 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

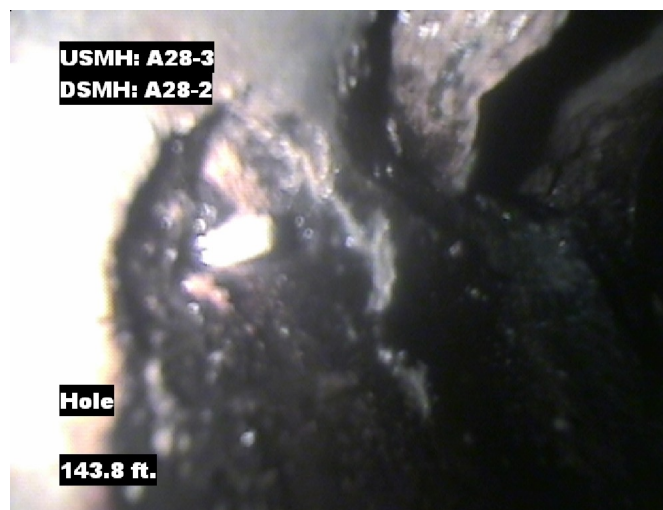


Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A28-3_A28-2	Oliver Springs	Highland Dr	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A28-3	Total Length 278.5	Year Laid	Shape Circular	Location Details	
DS Manhole A28-2	Length surveyed 278.5	Year Renewed	Height 8	Width 8	Pipe Joint... 4




Distance: 136.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 143.8 ft. Grade: 3
Condition: Hole
Remarks: N/A

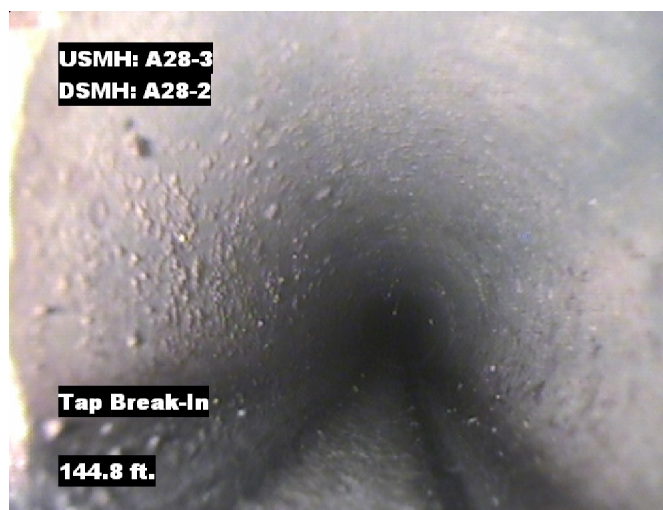

Distance: 144.8 ft. Grade: 0
Condition: Tap Break-In
Remarks: N/A

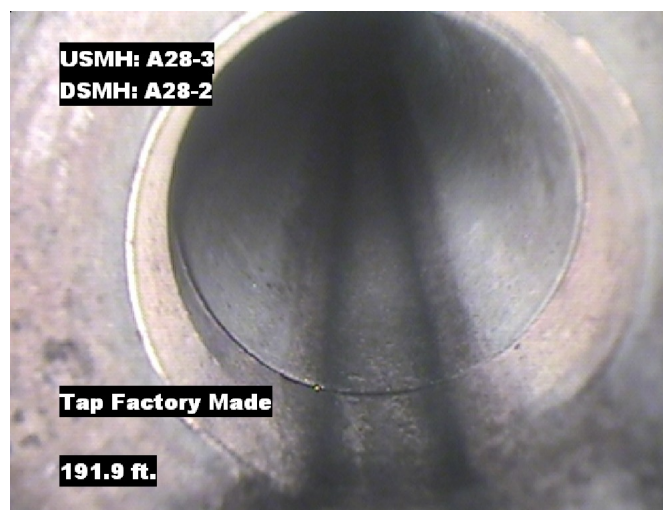


Distance: 191.9 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A28-3_A28-2	Oliver Springs	Highland Dr	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A28-3	Total Length 278.5	Year Laid	Shape Circular	Location Details	
DS Manhole A28-2	Length surveyed 278.5	Year Renewed	Height 8	Width 8	Pipe Joint... 4

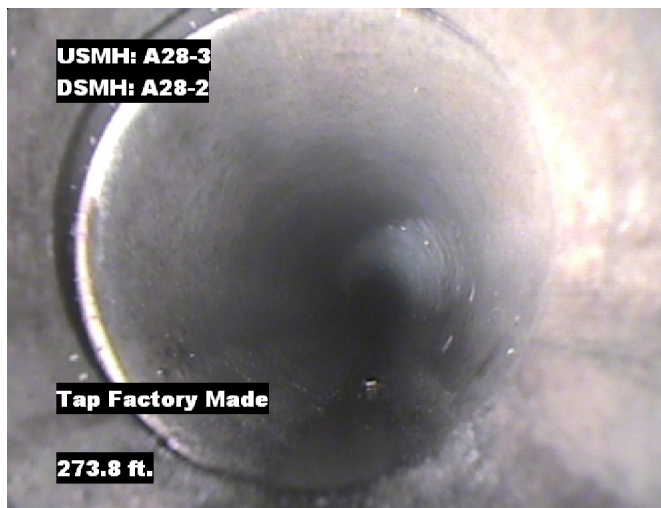

Distance: 273.8 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

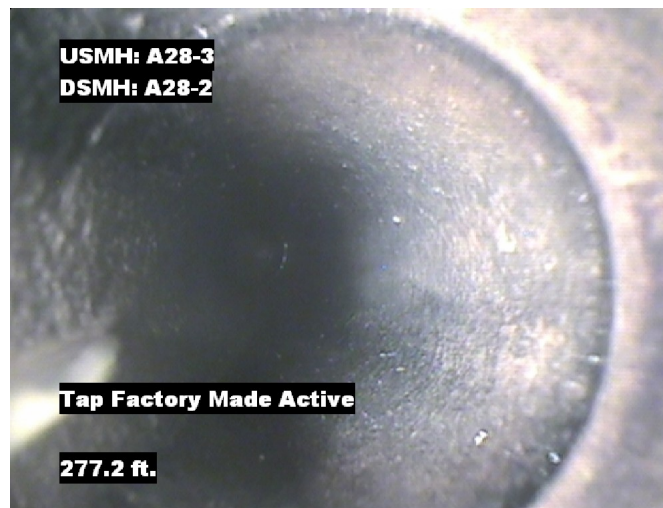

Distance: 277.2 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A

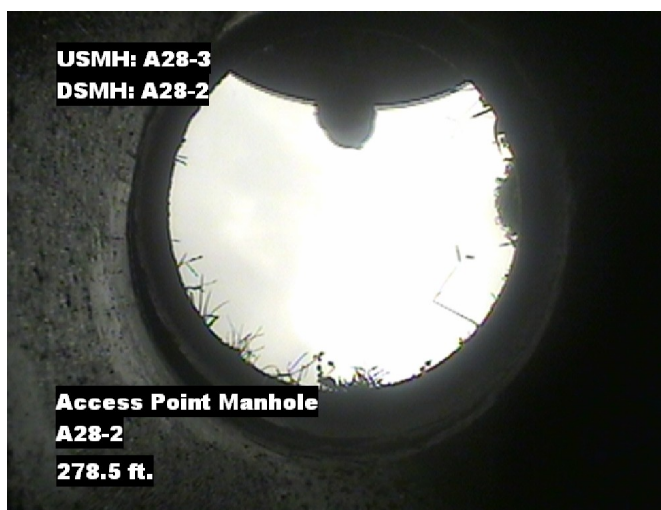

Distance: 278.5 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A28-2



ITpipes
4921 Alexander Blvd
Albuquerque, NM
505-341-0109

Pipe Segment Refere... A28-3_A28-2	City Oliver Springs	Street Highland Dr	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A28-3	Total Length 278.5	Year Laid	Shape Circular		Location Details	
DS Manhole A28-2	Length surveyed 278.5	Year Renewed	Height 8	Width 8	Pipe Joint...	
SPR 3	MPR N/A	PO Number 4397-03			Customer GRW	
SPRI 3	MPRI N/A	Work Order 4397-02			Purpose	
QSR 3100	QMR N/A	Pre-Rehabilitation Survey				
OPR 3	Surveyed By Charlie Gordon	Direction Downstream	Date 20150820		Media label	
OPRI 3	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 14:12		Weather Damp	
Date Cleaned 20150820			End Time 14:12		Additional Info	

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	1	3	3	0	0	3	1	3
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Code	ID	Length									
