



Defect Listing

Pipe Segment Refere... A39-3_A39-2	City Oliver Springs	Street Butler Mill Drive	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A39-3	Total Length 221.9	Year Laid	Shape Circular		Location Details	
DS Manhole A39-2	Length surveyed 221.9	Year Renewed	Height 8	Width 8	Pipe Joint... 4	


SPR 3	MPR N/A	PO Number 4397-03		Customer GRW	
SPRI 3	MPRI N/A	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR 3100	QMR N/A				
OPR 3	Surveyed By Barry_Rogers	Direction Downstream	Date 20150810	Media label	
OPRI 3	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 14:59	Weather Dry	
Date Cleaned 20150810			End Time 15:13	Additional Info	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A39-3									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
124.8 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
152.2 ft.	Hole				0	<input type="checkbox"/>	12		3
220.9 ft.	Tap Factory Made Active		8		0	<input type="checkbox"/>	6		
220.9 ft.	Water Level				5	<input type="checkbox"/>			
221.9 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A39-2									




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A39-3_A39-2	Oliver Springs	Butler Mill Drive	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH A39-3	Total Length 221.9	Year Laid	Shape Circular	Location Details	
DS Manhole A39-2	Length surveyed 221.9	Year Renewed	Height 8	Width 8	Pipe Joint... 4

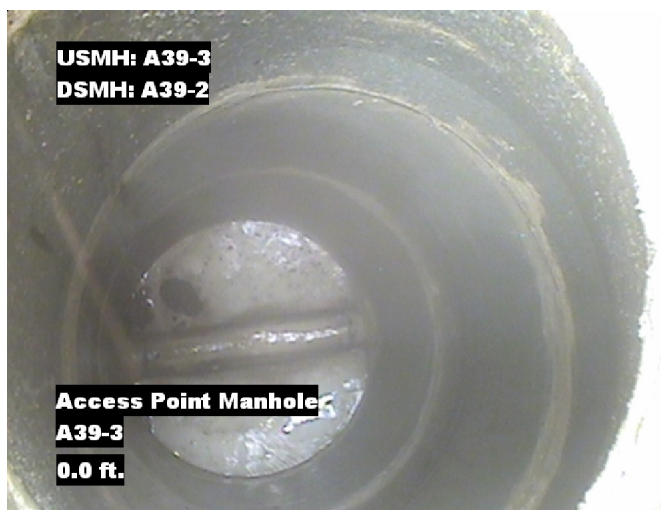


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A39-3

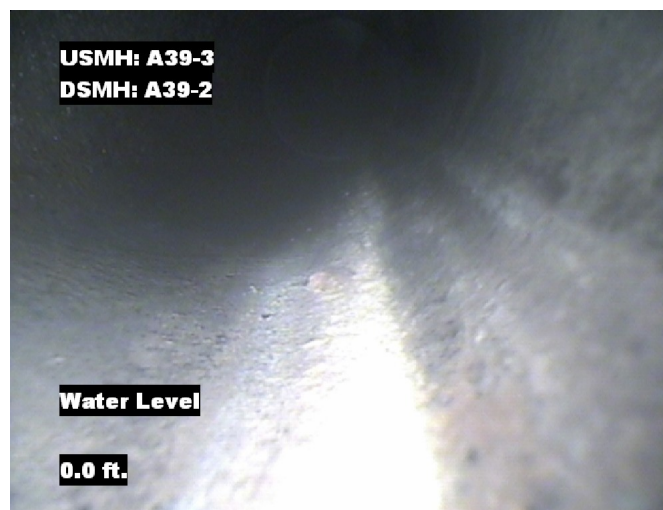

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

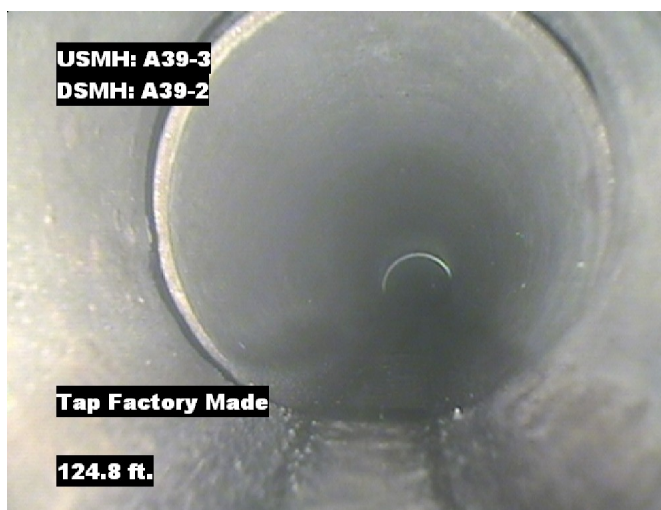

Distance: 124.8 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

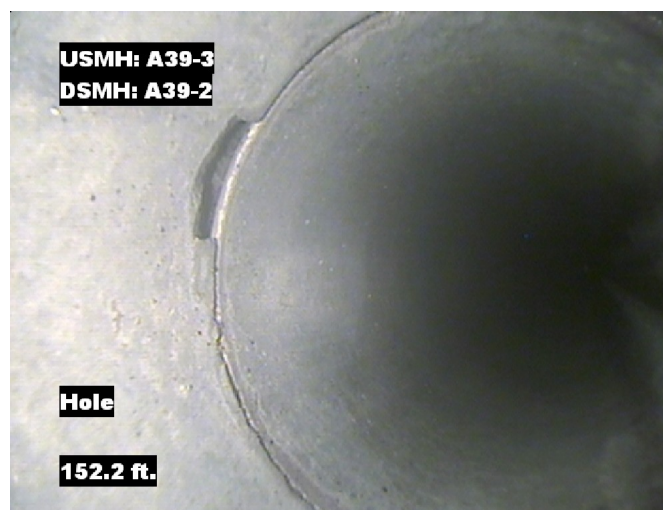


Distance: 152.2 ft. Grade: 3
Condition: Hole
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A39-3_A39-2	Oliver Springs	Butler Mill Drive	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A39-3	221.9		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A39-2	221.9		8	8	4

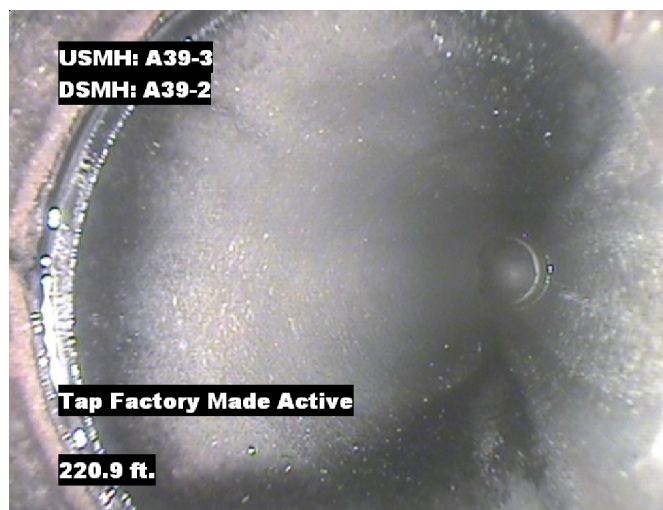

Distance: 220.9 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A

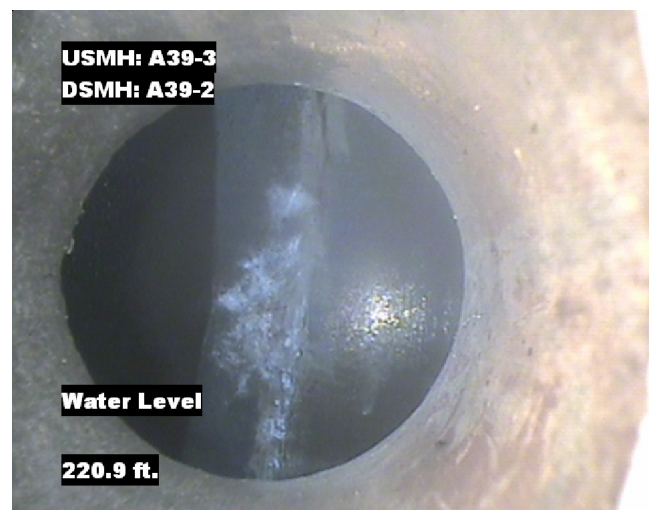

Distance: 220.9 ft. Grade: 0
Condition: Water Level
Remarks: N/A

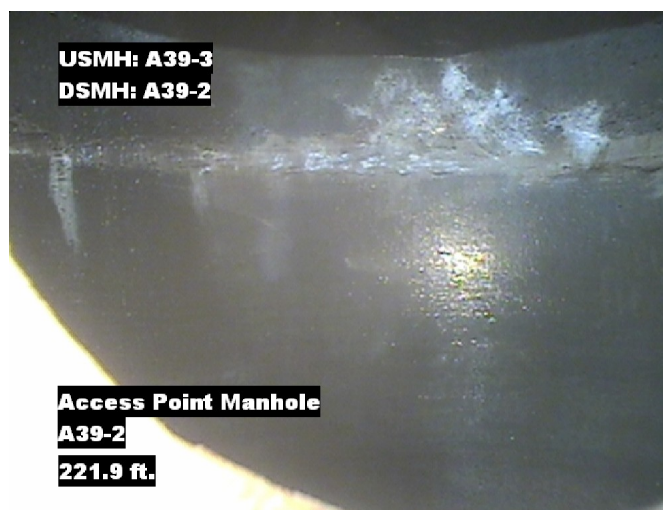

Distance: 221.9 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A39-2



PACP Conditions

Pipe Segment Refere... A39-3_A39-2	City Oliver Springs	Street Butler Mill Drive	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A39-3	Total Length 221.9	Year Laid	Shape Circular	Location Details	
DS Manhole A39-2	Length surveyed 221.9	Year Renewed	Height 8	Width 8	Pipe Joint... 4
SPR 3	MPR N/A	PO Number 4397-03		Customer GRW	
SPRI 3	MPRI N/A	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR 3100	QMR N/A	Direction Downstream		Date 20150810	
OPR 3	Surveyed By Barry Rogers	Pre-Cleaning Jetting		Media label	
OPRI 3	Certificate Number U-1012-16405	Time 14:59		Weather Dry	
Date Cleaned 20150810			End Time 15:13		Additional Info

Normal Defects			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	1	3	3	0	0	3	1	3
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Code	ID	Length									
