



Defect Listing

Pipe Segment Refere... A6-19_A6-19A	City Oliver Springs	Street Highway 61	Material Concrete Pipe (non-...	Location C... Main Highw...	Sewer Use Sanitary
Upstream MH A6-19	Total Length 48.7	Year Laid	Shape Circular	Location Details	
DS Manhole A6-19A	Length surveyed 48.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4


SPR N/A	MPR N/A	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI N/A	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR N/A				
OPR N/A	Surveyed By Charlie Gordon	Direction Downstream	Date 20150820	Media label	
OPRI N/A	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 13:20	Weather Damp	
Date Cleaned 20150820			End Time 13:24	Additional Info	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A6-19A									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
47.4 ft.	Water Level				5	<input type="checkbox"/>			
48.7 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A6-19									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A6-19_A6-19A	Oliver Springs	Highway 61	Concrete Pipe (non-...	Main Highw...	Sanitary
Upstream MH A6-19	Total Length 48.7	Year Laid	Shape Circular	Location Details	
DS Manhole A6-19A	Length surveyed 48.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4

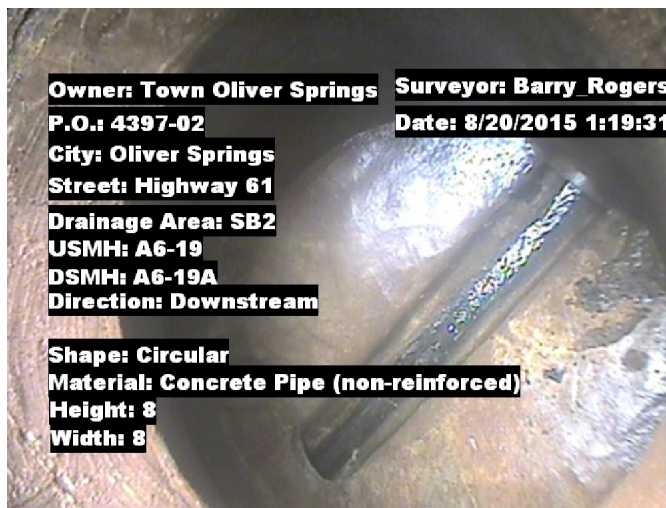

Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A6-19A




Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

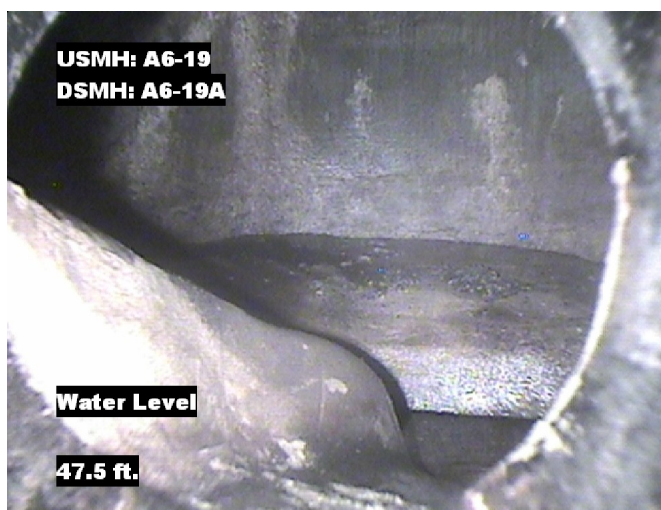

Distance: 47.4 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 48.7 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A6-19



Pipe Segment Refere...		City	Street	Material		Location C...		Sewer Use
A6-19_A6-19A		Oliver Springs	Highway 61	Concrete Pipe (non-...		Main Highw...		Sanitary
Upstream MH		Total Length	Year Laid	Shape		Location Details		
A6-19		48.7		Circular				
DS Manhole		Length surveyed	Year Renewed	Height	Width	Pipe Joint...		
A6-19A		48.7		8	8	4		
SPR	N/A	MPR	N/A	PO Number		Customer		
SPRI	N/A	MPRI	N/A	4397-03		GRW		
QSR	N/A	QMR	N/A	Work Order		Purpose		
				4397-02		Pre-Rehabilitation Survey		
OPR	N/A	Surveyed By	Direction	Date		Media label		
		Charlie Gordon	Downstream	20150820				
OPRI	N/A	Certificate Number	Pre-Cleaning	Time		Weather		
		U-615-07000491	Jetting	13:20		Damp		
Date Cleaned				End Time		Additional Info		
20150820				13:24				

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
<div>Continuous Defects</div> <div>CodeIDLength</div>			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
			Subtotals	0		Subtotals	0		Subtotals	0	
SUMMARY			Pipe Rating	0		Pipe Rating	0		Overall Pipe Rating	0	
			Structural Index	0		O&M Index	0		Overall Index	0	
			Str. Quick Rating	0000		O&M Quick Rating	0000		Ovrl. Quick Rating	0000	
