



Defect Listing

Pipe Segment Refere... A6-6A_A6-6	City Oliver Springs	Street Tri county boulevard...	Material Concrete Pipe (non-...	Location C... Easement/R...	Sewer Use Sanitary
Upstream MH A6-6A	Total Length 115.7	Year Laid	Shape Circular	Location Details	
DS Manhole A6-6	Length surveyed 115.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4

SPR 5	MPR 5	PO Number 4397-03	Customer GRW
SPRI 5	MPRI 2.5	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR 5100	QMR 3121		
OPR 10	Surveyed By Charlie Gordon	Direction Downstream	Date 20150826
OPRI 3.3	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 10:43
	Date Cleaned 20150826	End Time 10:51	Weather Dry
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A6-6A									
0.0 ft.	Water Level				10	<input type="checkbox"/>			
27.5 ft.	Tap Factory Made Active		6		0	<input type="checkbox"/>	3		
81.5 ft.	Water Level Sag				20	<input type="checkbox"/>			2
81.5 ft.	Material Change				0	<input type="checkbox"/>			
Remarks: CP TO PVC									
85.2 ft.	Material Change				0	<input type="checkbox"/>			
Remarks: PVC TO CP									
87.5 ft.	Hole Soil Visible				0	<input type="checkbox"/>	9		5
87.5 ft.	Infiltration Dripper				0	<input type="checkbox"/>	9		3
113.0 ft.	Water Level				5	<input type="checkbox"/>			
115.7 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A6-6									



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A6-6A_A6-6	Oliver Springs	Tri county boulevard...	Concrete Pipe (non-...	Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A6-6A	115.7		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A6-6	115.7		8	8	4




Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A6-6A



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 27.5 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A

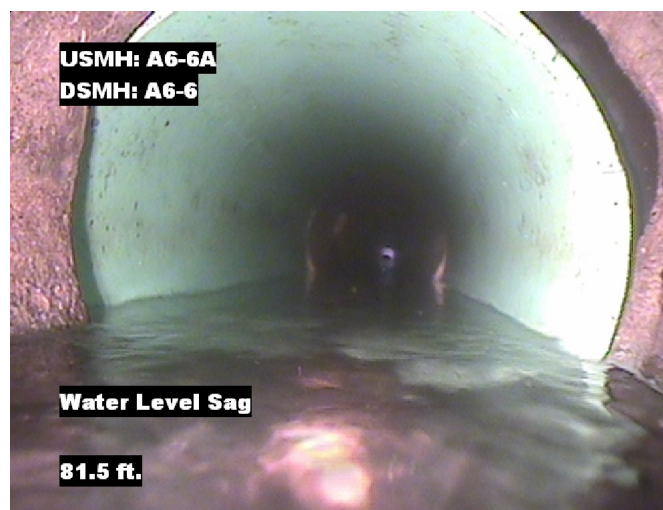


Distance: 81.5 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A6-6A_A6-6	Oliver Springs	Tri county boulevard...	Concrete Pipe (non-...	Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A6-6A	115.7		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A6-6	115.7		8	8	4

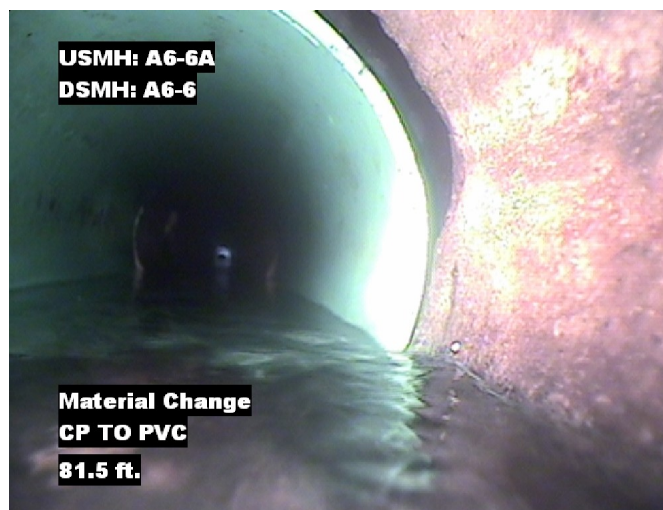


Distance: 81.5 ft. Grade: 0
Condition: Material Change
Remarks: CP TO PVC

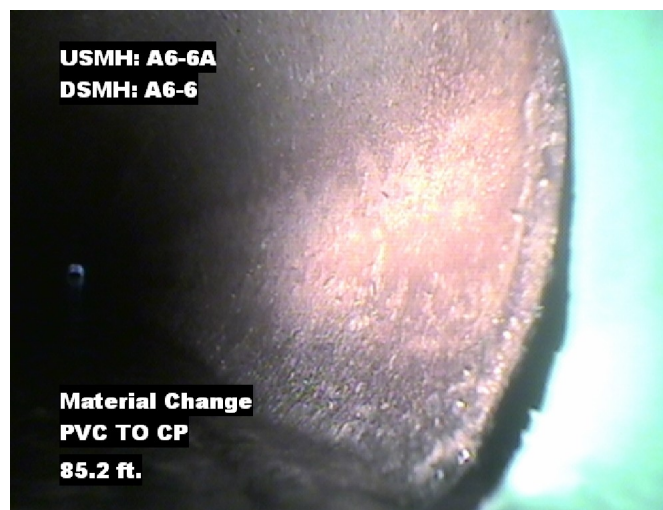

Distance: 85.2 ft. Grade: 0
Condition: Material Change
Remarks: PVC TO CP

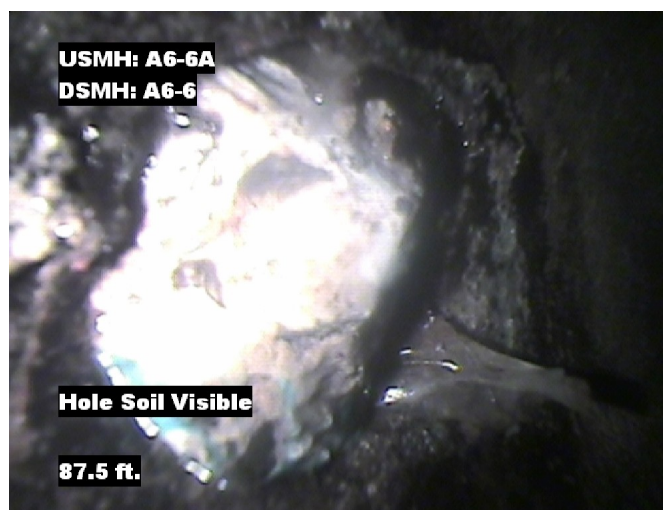

Distance: 87.5 ft. Grade: 5
Condition: Hole Soil Visible
Remarks: N/A

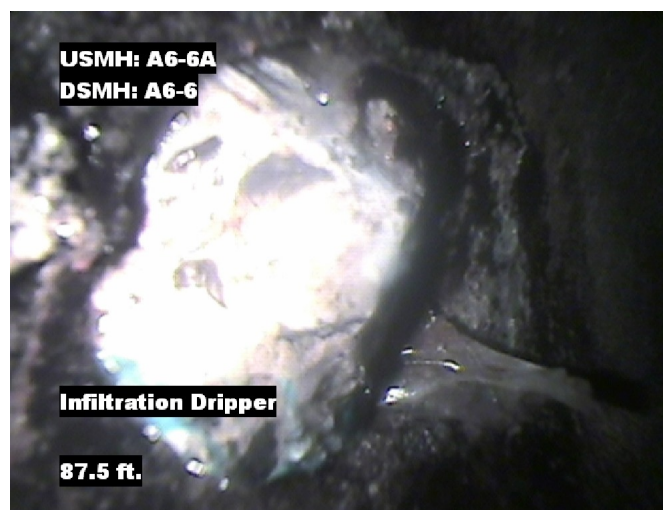

Distance: 87.5 ft. Grade: 3
Condition: Infiltration Dripper
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere... A6-6A_A6-6	City Oliver Springs	Street Tri county boulevard...	Material Concrete Pipe (non-...		Location C... Easement/R...	Sewer Use Sanitary
Upstream MH A6-6A	Total Length 115.7	Year Laid	Shape Circular		Location Details	
DS Manhole A6-6	Length surveyed 115.7	Year Renewed	Height 8	Width 8	Pipe Joint...	4



Distance: 113.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 115.7 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A6-6



Pipe Segment Refere... A6-6A_A6-6	City Oliver Springs	Street Tri county boulevard...	Material Concrete Pipe (non-...		Location C... Easement/R...	Sewer Use Sanitary
Upstream MH A6-6A	Total Length 115.7	Year Laid	Shape Circular		Location Details	
DS Manhole A6-6	Length surveyed 115.7	Year Renewed	Height 8	Width 8	Pipe Joint... 4	
SPR 5	MPR 5	PO Number 4397-03		Customer GRW		
SPRI 5	MPRI 2.5	Work Order 4397-02		Purpose		
QSR 5100	QMR 3121			Pre-Rehabilitation Survey		
OPR 10	Surveyed By Charlie Gordon	Direction Downstream	Date 20150826		Media label	
OPRI 3.3	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 10:43		Weather Dry	
Date Cleaned 20150826			End Time 10:51		Additional Info	

Page #: 5
