



Defect Listing

Pipe Segment Refere... A8-11_A8-10	City Oliver Springs	Street Railroad Ave	Material Fibreglass Reinforc...	Location C... Light High...	Sewer Use Sanitary
Upstream MH A8-11	Total Length 325.4	Year Laid	Shape Circular	Location Details	
DS Manhole A8-10	Length surveyed 325.4	Year Renewed	Height 8	Width 8	Pipe Joint... N/A


SPR N/A	MPR 5	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 2.5	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 3121		
OPR 5	Surveyed By Barry Rogers	Direction Downstream	Date 20150731
OPRI 2.5	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 09:06
	Date Cleaned 20150731	End Time 09:24	Weather Dry
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A8-11									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
39.8 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
153.1 ft.	Deposits Attached Grease				5	<input type="checkbox"/>	9		2
227.6 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
227.6 ft.	Infiltration Dripper				0	<input type="checkbox"/>	1		3
322.8 ft.	Water Level				10	<input type="checkbox"/>			
325.4 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: A8-10									




Image Report 4/Page


Pipe Segment Refere... A8-11_A8-10	City Oliver Springs	Street Railroad Ave	Material Fibreglass Reinforc...		Location C... Light High...	Sewer Use Sanitary
Upstream MH A8-11	Total Length 325.4	Year Laid	Shape Circular		Location Details	
DS Manhole A8-10	Length surveyed 325.4	Year Renewed	Height 8	Width 8	Pipe Joint...	N/A

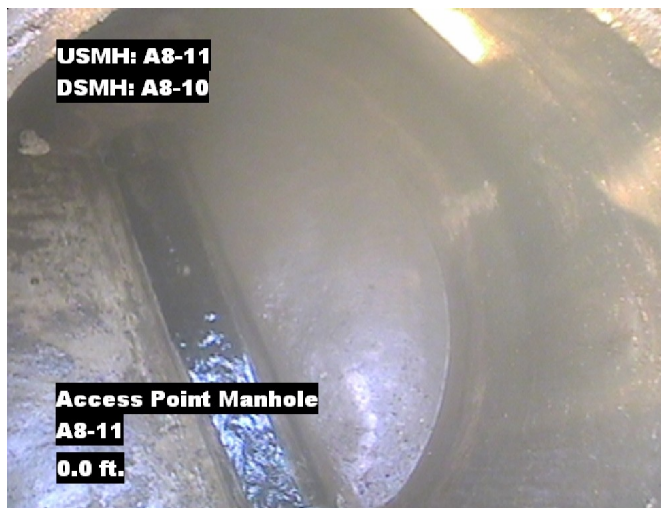

Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A8-11

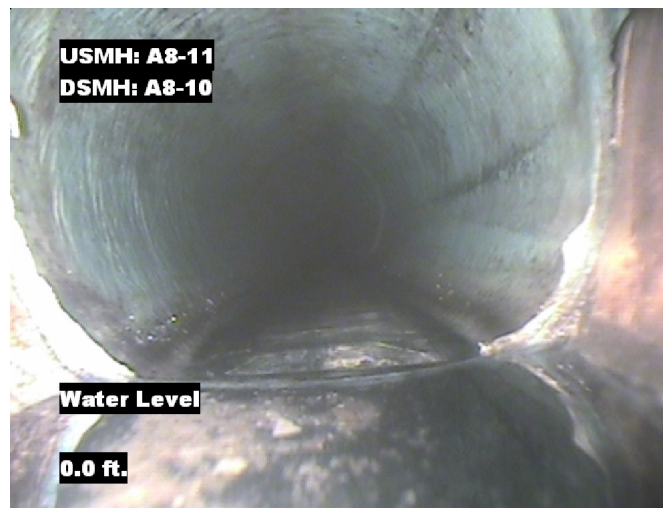

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

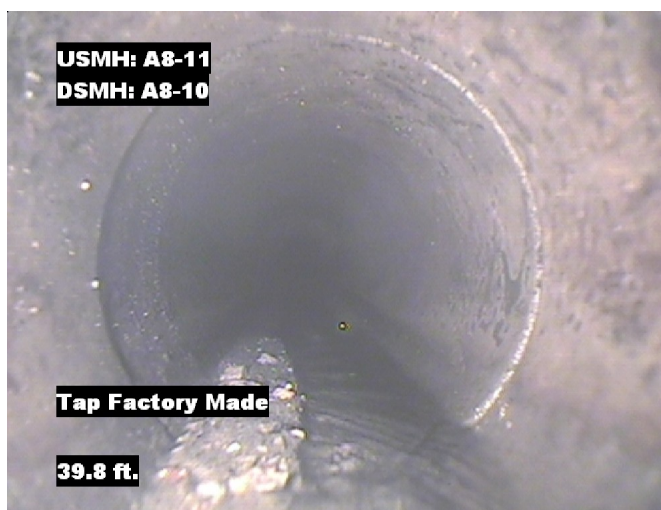

Distance: 39.8 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Distance: 153.1 ft. Grade: 2
Condition: Deposits Attached Grease
Remarks: N/A



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A8-11_A8-10	Oliver Springs	Railroad Ave	Fibreglass Reinforc...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A8-11	325.4		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A8-10	325.4		8	8	N/A

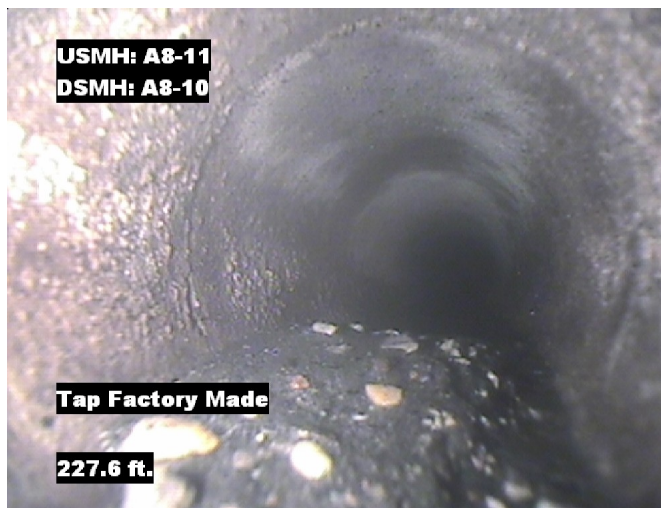


Distance: 227.6 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 227.6 ft. Grade: 3
Condition: Infiltration Dripper
Remarks: N/A

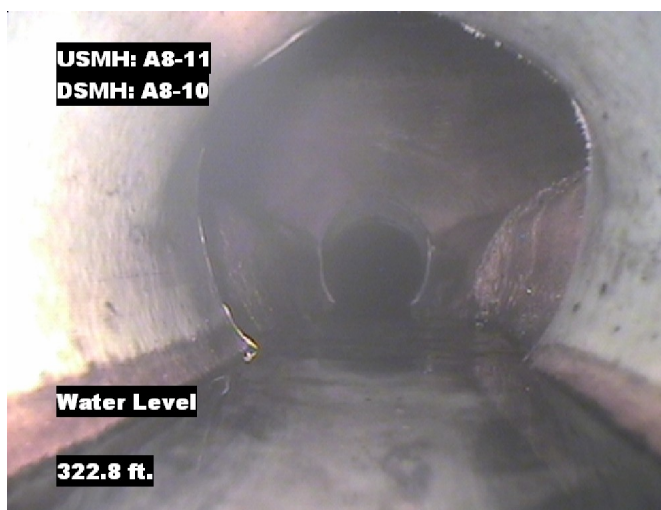

Distance: 322.8 ft. Grade: 0
Condition: Water Level
Remarks: N/A

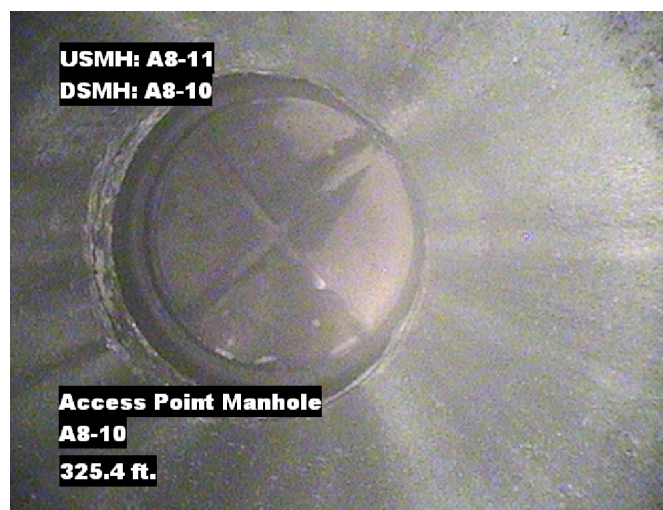

Distance: 325.4 ft. Grade: 0
Condition: Access Point Manhole
Remarks: A8-10



PACP Conditions

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
A8-11_A8-10	Oliver Springs	Railroad Ave	Fibreglass Reinforc...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
A8-11	325.4		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
A8-10	325.4		8	8	N/A
SPR	N/A	MPR	5	Customer	
SPRI	N/A	MPRI	2.5	GRW	
QSR	N/A	QMR	3121	Purpose	
				Pre-Rehabilitation Survey	
OPR	Surveyed By	Direction	Date	Media label	
5	Barry_Rogers	Downstream	20150731		
OPRI	Certificate Number	Pre-Cleaning	Time	Weather	
2.5	U-1012-16405	Jetting	09:06	Dry	
Date Cleaned			End Time	Additional Info	
20150731			09:24		

[illegible]
