

Defect Listing

Pipe Segment Refere		City		Street	Mat	erial	Location C	Sewer Use	
A8-13_A8-12		Oliver Springs		Walden rd	Concrete F	ipe (non	Yard	Sanitary	
Upstream MH A8-13 DS Manhole		Total Length 188.2 Length surveyed		Year Laid	Shape		Location Details		
					Circ	Circular			
				Year Renewed	Height Width		Pipe Joint		
A8	A8-12		8.2		8	8	4		
SPR	N/A	MPR 14		PO Number			Customer		
	-			4397-03	Pre-F		GRW		
SPRI	N/A	MPRI	2.8	Work Order			Purpose		
QSR	N/A	QMR	4223	4397-02			-Rehabilitation Survey		
Ol	PR	Surve	yed By	Direction	Date		Media label		
1	4	Barry_	Rogers	Downstream	20150731				
OF	PRI	Certificate Number		Pre-Cleaning	Time		Weather		
2.8		U-1012-16405		Heavy Cleaning	07:54		Dry		
		Date C	Cleaned	End Time		Additional Info			
		2015	50731	08:25					

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Cuada
Distalle	Condition	Cont. Dict.	1st	2nd	%	Joint	At/From	То	Grade
0.0 ft.	Access Point Manhole				0				
Remarks:	A8-13								•
0.0 ft.	Water Level				5				
74.5 ft.	Infiltration Runner				0		6		4
89.5 ft.	Tap Factory Made		6		0		12		
170.0 ft.	Deposits Attached Grease				5		9	12	2
175.6 ft.	Deposits Attached Grease				10		3		2
176.1 ft.	Water Level Sag				20				2
177.1 ft.	Camera Underwater				0				4
185.6 ft.	Water Level				5				
188.2 ft.	Access Point Manhole				0				
Remarks:	A8-12								•





Image Report 4/Page

Pipe Segment Refere	City	Street	Material		Location C	Sewer Use
A8-13_A8-12	Oliver Springs	Walden rd	Concrete Pipe (non		Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape		Location	
A8-13	188.2		Circ	ular		
DS Manhole	Length surveyed	Year Renewed	Height Width		Pipe Joint	
A8-12	188.2		8	8	4	



Distance: 0.0 ft. Grade: (

Condition: Access Point Manhole

Remarks: A8-13



Distance: 0.0 ft. Grade: 0

Condition: Water Level

Remarks: N/A



Distance: 74.5 ft. Grade: 4

Condition: Infiltration Runner

Remarks: N/A



Distance: 89.5 ft. Grade: 0

Condition: Tap Factory Made


Remarks: N/A





Image Report 4/Page

Pipe Segment Refere	City	Street	Material		Location C	Sewer Use
A8-13_A8-12	A8-13_A8-12 Oliver Springs Walden rd Co		Concrete Pipe (non		Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape		Location	Details
A8-13	188.2		Circ	ular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint	
A8-12	188.2		8	8	4	

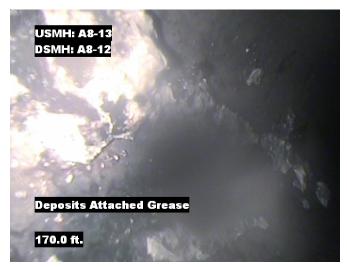

Distance: 170.0 ft. Grade: 2
Condition: Deposits Attached Grease

Remarks: N/A




Distance: 175.6 ft. **Grade**: 2

Deposits Attached Grease

Remarks: N/A

Condition:

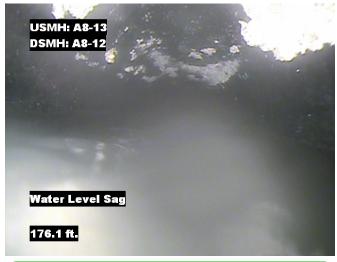

Distance: 176.1 ft. Grade: 2

Condition: Water Level Sag

Remarks: N/A



Distance: 177.1 ft. Grade: 4

Condition: Camera Underwater


Remarks: N/A

ITpipes 4921 Alexander Blvd Albuquerque, NM 505-341-0109



Image Report 4/Page

Pipe Segment Refere	City	Street	Material		Location C	Sewer Use
A8-13_A8-12	Oliver Springs	Walden rd	Concrete Pipe (non		Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape		Location	Details
A8-13	188.2		Circular			
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint	
A8-12	188.2		8	8	4	

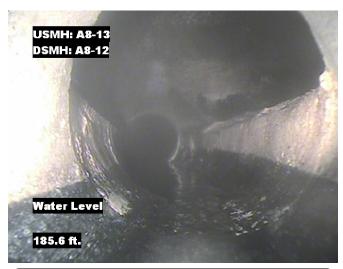

Distance: 185.6 ft. Grade: 0

Condition: Water Level

Remarks: N/A



Distance: 188,2 ft. Grade: 0

Condition: Access Point Manhole

Remarks: A8-12



PACP Conditions

Pipe Segment Refere		City		Street	Mat	erial	Location C	Sewer Use	
A8-13_A8-12		Oliver	Springs	Walden rd	Concrete F	Pipe (non	Yard	Sanitary	
Upstream MH To		Total I	Length	Year Laid	Sh	ape	Location Details		
A8-13		188.2			Circ	cular			
DS Ma	DS Manhole Length su		surveyed	Year Renewed	Height	Width	Pipe Joint		
A8-	A8-12		8.2		8	8	4		
SPR	N/A	MPR	14	PO Number			Customer		
SPRI	N/A	MPRI	2.8	4397-03					
SFRI	IN/A	IVIFKI	2.0	Work Order			Purpose		
QSR	N/A	QMR	4223	4397-02		Pre-		urvey	
OF	PR	Surve	yed By	Direction [Date Med		dia label	
1	4	Barry_Rogers		Downstream	20150731				
OF	OPRI		e Number	Pre-Cleaning	Time		Weather		
2.8		U-1012-16405		Heavy Cleaning	07:54		Dry		
		Date C	Cleaned	End Time		Additional Info			
		2015	0731	08:25					

	Structural Ratings			0	& M Ratin	gs	Con	nbined Ra	tings
Normal Defects	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
	1	0	0	1	0	0	1	0	0
	2	0	0	2	3	6	2	3	6
	3	0	0	3	0	0	3	0	0
	4	0	0	4	2	8	4	2	8
	5	0	0	5	0	0	5	0	0
Continuous Defects Code ID Length									
	Subtotals	0		Subtotals	5		Subtotals	5	
SUMMARY	Struct	Pipe Rating 0 ructural Index 0 Quick Rating 0000		Pipe Rating O&M Index O&M Quick Rating		14 2.8 4223	Overall Pipe Rating Overall Index Ovrl. Quick Rating		14 2.8 4223
