



Defect Listing

Pipe Segment Refere... B3-4_B3-3	City Oliver Springs	Street Kentucky St	Material Concrete Pipe (non-...	Location C... Light High...	Sewer Use Sanitary
Upstream MH B3-4	Total Length 235.1	Year Laid	Shape Circular	Location Details	
DS Manhole B3-3	Length surveyed 235.1	Year Renewed	Height 8	Width 8	Pipe Joint... 4


SPR N/A	MPR 2	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 2	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 2100		
OPR 2	Surveyed By Charlie Gordon	Direction Upstream	Date 20150908
OPRI 2	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 13:08
	Date Cleaned 20150908	End Time 13:25	Weather Dry
		Additional Info	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: B3-3									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
20.1 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
23.1 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
90.6 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
120.3 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
120.9 ft.	Water Level Sag				10	<input type="checkbox"/>			2
215.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
229.1 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
235.1 ft.	Survey Abandoned				0	<input type="checkbox"/>			
Remarks: COMPLETE LINE									




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
B3-4_B3-3	Oliver Springs	Kentucky St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
B3-4	235.1		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
B3-3	235.1		8	8	4

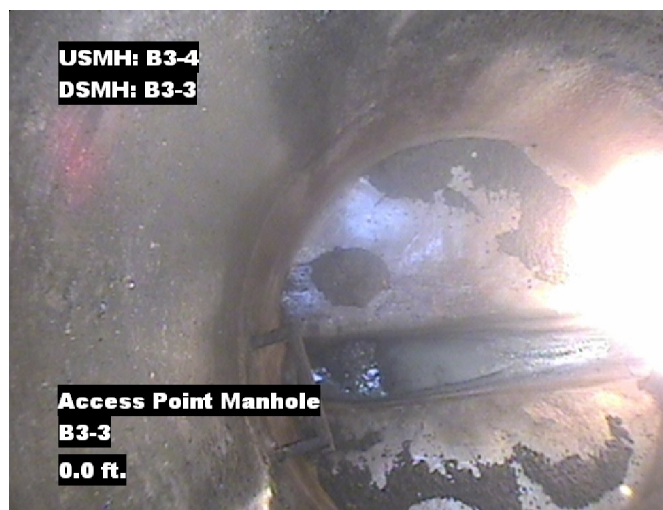


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: B3-3

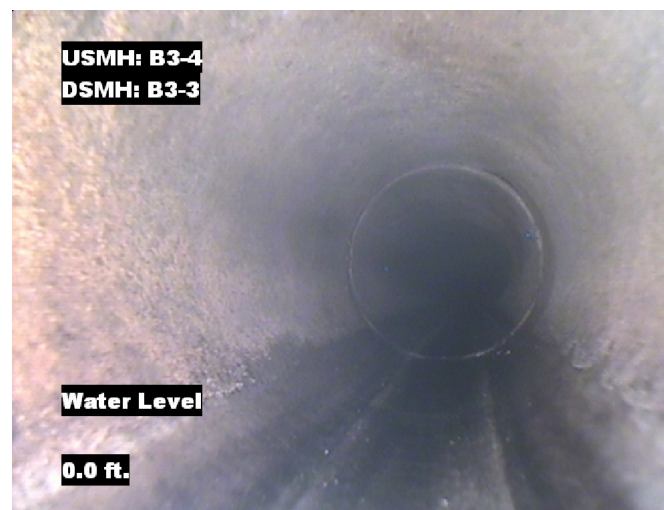

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

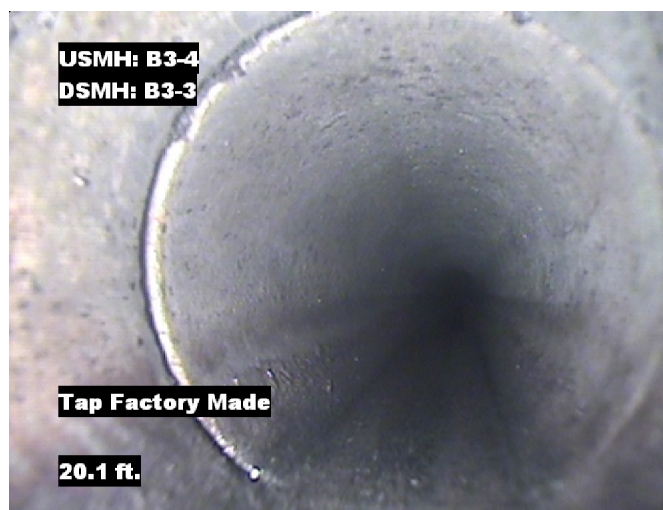

Distance: 20.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

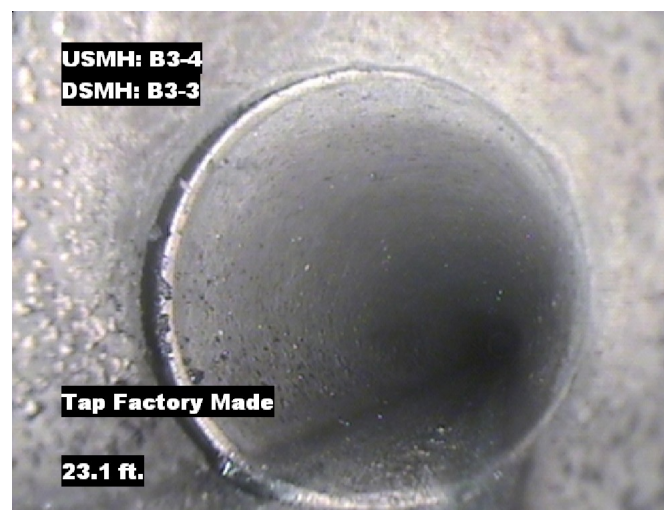


Distance: 23.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
B3-4_B3-3	Oliver Springs	Kentucky St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
B3-4	235.1		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
B3-3	235.1		8	8	4

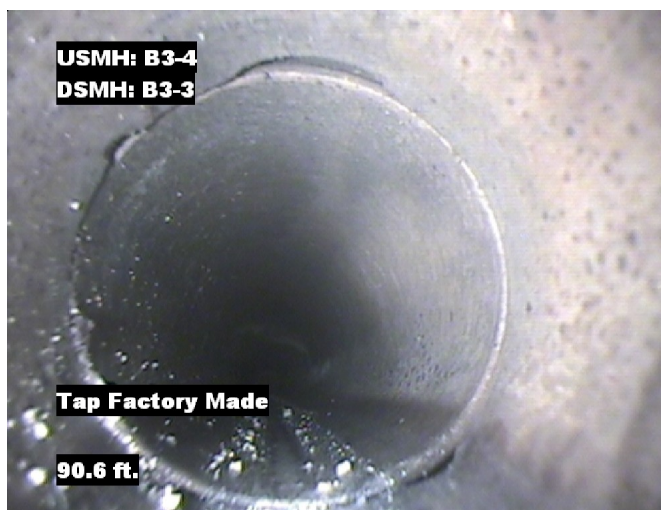


Distance: 90.6 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

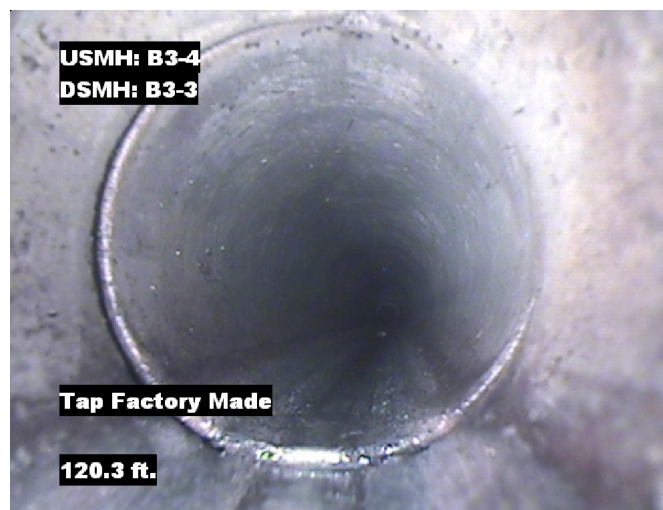

Distance: 120.3 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 120.9 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A

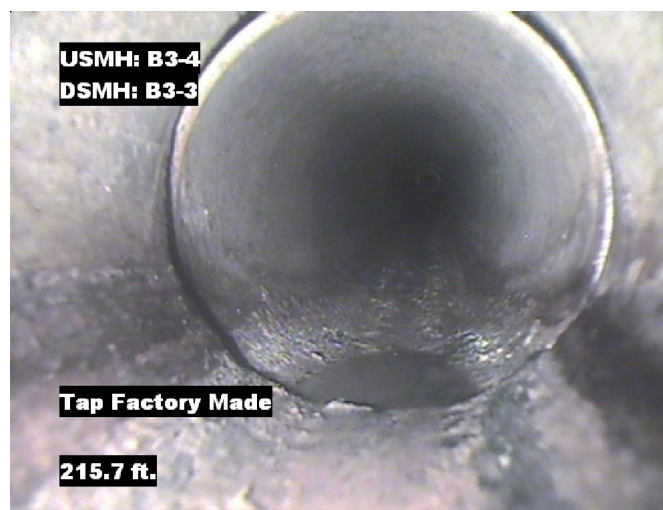


Distance: 215.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
B3-4_B3-3	Oliver Springs	Kentucky St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH B3-4	Total Length 235.1	Year Laid	Shape Circular	Location Details	
DS Manhole B3-3	Length surveyed 235.1	Year Renewed	Height 8	Width 8	Pipe Joint... 4

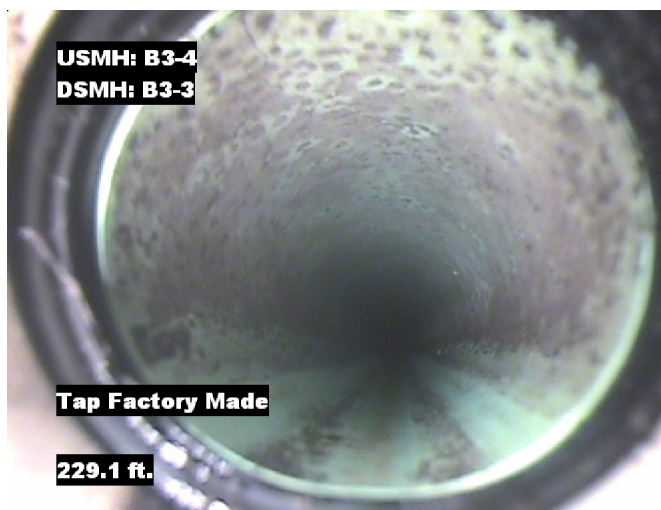

Distance: 229.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

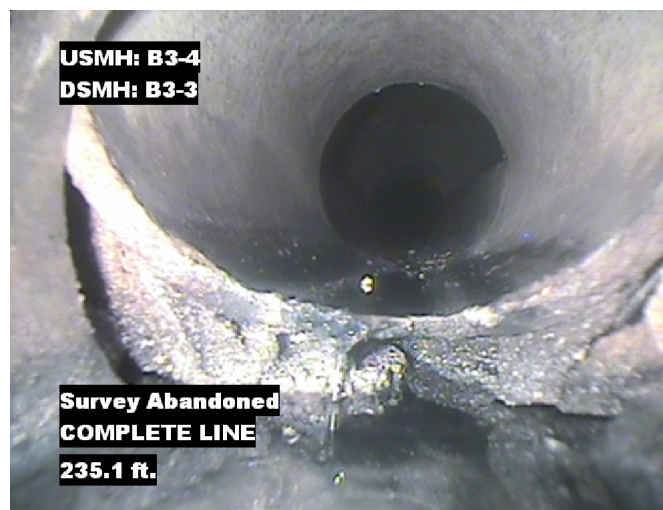

Distance: 235.1 ft. Grade: 0
Condition: Survey Abandoned
Remarks: COMPLETE LINE



Pipe Segment Refere... B3-4_B3-3	City Oliver Springs	Street Kentucky St	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH B3-4	Total Length 235.1	Year Laid	Shape Circular		Location Details	
DS Manhole B3-3	Length surveyed 235.1	Year Renewed	Height 8	Width 8	Pipe Joint... 4	
SPR N/A	MPR 2	PO Number 4397-03		Customer GRW		
SPRI N/A	MPRI 2	Work Order 4397-02		Purpose		
QSR N/A	QMR 2100			Pre-Rehabilitation Survey		
OPR 2	Surveyed By Charlie_Gordon	Direction Upstream	Date 20150908		Media label	
OPRI 2	Certificate Number U-615-07000491	Pre-Cleaning Jetting	Time 13:08		Weather Dry	
Date Cleaned 20150908			End Time 13:25		Additional Info	

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	1	2	2	1	2
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Code	ID	Length									
