



Defect Listing

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D-15_D-14	Oliver Springs	Midway Dr	Fibreglass Reinforc...	Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D-15	351.1		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D-14	351.1		10	10	N/A


SPR	N/A	MPR	N/A	PO Number	Customer
SPRI	N/A	MPRI	N/A	4397-03	GRW
QSR	N/A	QMR	N/A	Work Order	Purpose
				4397-02	Pre-Rehabilitation Survey
OPR	Surveyed By	Direction	Date	Media label	
N/A	Barry Rogers	Downstream	20150707		
OPRI	Certificate Number	Pre-Cleaning	Time	Weather	
N/A	U-1012-16405	Jetting	08:08	Dry	
Date Cleaned			End Time	Additional Info	
20150707			08:27		

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D-15									
0.0 ft.	Water Level				15	<input type="checkbox"/>			
56.0 ft.	Water Level				35	<input type="checkbox"/>			
121.9 ft.	Water Level				55	<input type="checkbox"/>			
175.6 ft.	Tap Factory Made Active		6		0	<input type="checkbox"/>	9		
237.6 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
315.5 ft.	Water Level				35	<input type="checkbox"/>			
348.2 ft.	Water Level				25	<input type="checkbox"/>			
351.1 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D-14									




Image Report 4/Page


Pipe Segment Refere... D-15_D-14	City Oliver Springs	Street Midway Dr	Material Fibreglass Reinforc...		Location C... Yard	Sewer Use Sanitary
Upstream MH D-15	Total Length 351.1	Year Laid	Shape Circular		Location Details	
DS Manhole D-14	Length surveyed 351.1	Year Renewed	Height 10	Width 10	Pipe Joint...	
					N/A	

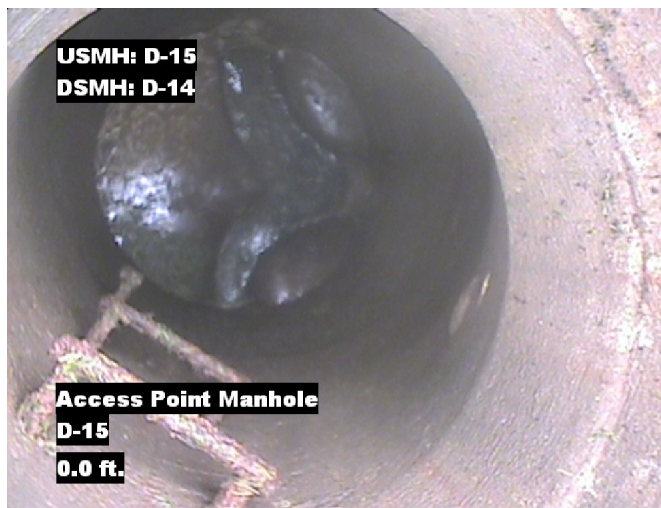


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D-15

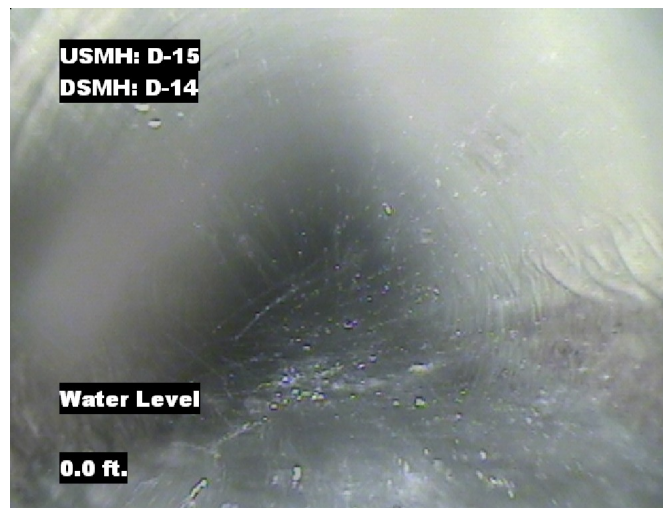

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

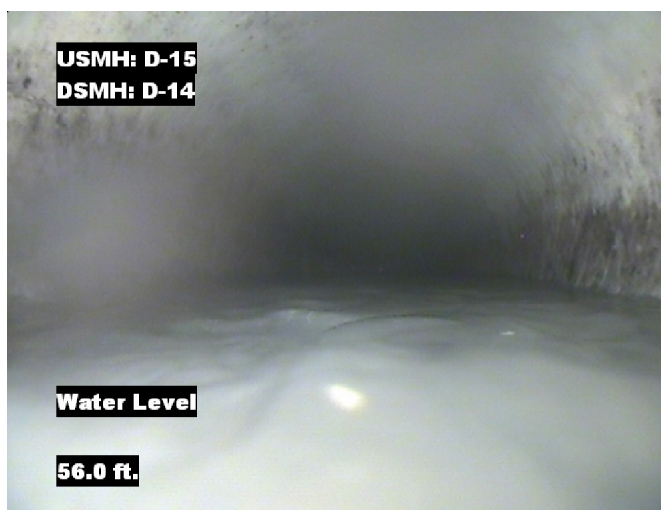

Distance: 56.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

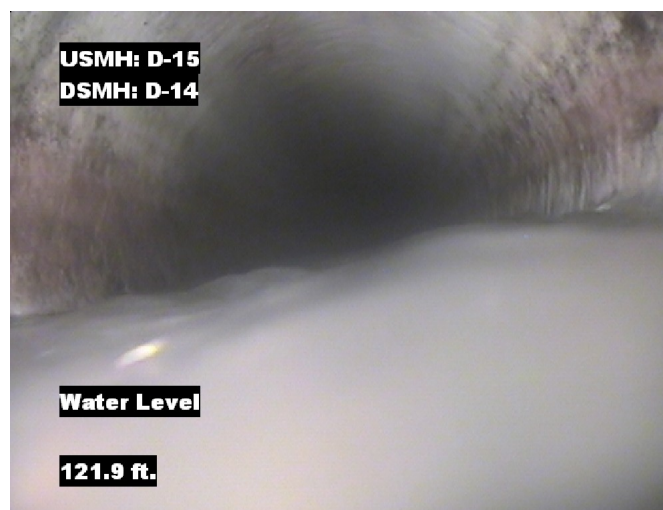


Distance: 121.9 ft. Grade: 0
Condition: Water Level
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D-15_D-14	Oliver Springs	Midway Dr	Fibreglass Reinforc...	Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D-15	351.1		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D-14	351.1		10	10	N/A

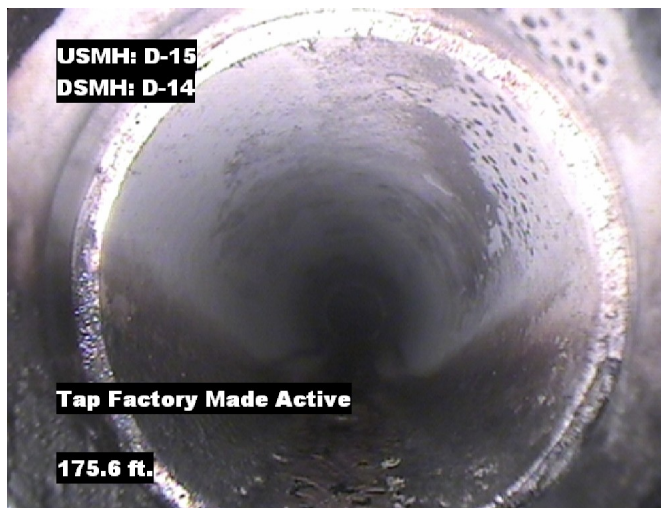

Distance: 175.6 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A

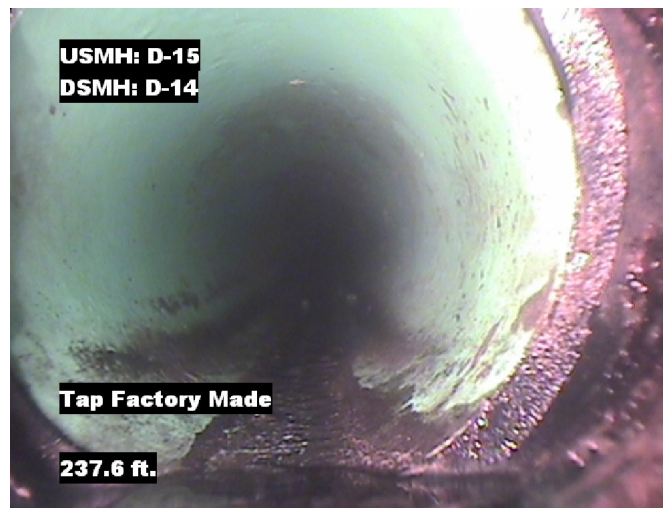

Distance: 237.6 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 315.5 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 348.2 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D-15_D-14	Oliver Springs	Midway Dr	Fibreglass Reinforc...	Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D-15	351.1		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D-14	351.1		10	10	N/A



Distance: 351.1 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D-14



PACP Conditions

Pipe Segment Refere... D-15_D-14	City Oliver Springs	Street Midway Dr	Material Fibreglass Reinforc...	Location C... Yard	Sewer Use Sanitary
Upstream MH D-15	Total Length 351.1	Year Laid	Shape Circular	Location Details	
DS Manhole D-14	Length surveyed 351.1	Year Renewed	Height 10	Width 10	Pipe Joint... N/A
SPR N/A	MPR N/A	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI N/A	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR N/A	Direction Downstream		Date 20150707	
OPR N/A	Surveyed By Barry Rogers	Pre-Cleaning Jetting		Time 08:08	
OPRI N/A	Certificate Number U-1012-16405	Date Cleaned 20150707		End Time 08:27	
			Media label		Weather Dry
			Additional Info		

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Continuous Defects											
Code	ID	Length									
			Subtotals	0		Subtotals	0		Subtotals	0	
SUMMARY			Pipe Rating	0		Pipe Rating	0		Overall Pipe Rating	0	
			Structural Index	0		O&M Index	0		Overall Index	0	
			Str. Quick Rating	0000		O&M Quick Rating	0000		Ovrl. Quick Rating	0000	
