



Defect Listing

Pipe Segment Refere... D19-8_D19-7	City Oliver Springs	Street Sleepy Hollow	Material Concrete Pipe (non-...	Location C... Yard	Sewer Use Sanitary
Upstream MH D19-8	Total Length 262.2	Year Laid	Shape Circular	Location Details	
DS Manhole D19-7	Length surveyed 262.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4

SPR 3	MPR 4	PO Number 4397-03	Customer GRW
SPRI 3	MPRI 4	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR 3100	QMR 4100		
OPR 7	Surveyed By Barry Rogers	Direction Downstream	Date 20150630
OPRI 3.5	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 08:13
	Date Cleaned 20150630	End Time 08:43	Weather Damp
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D19-7(D19-8)									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
38.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	10		
68.3 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	2		
151.0 ft.	Tap Break-In		6		0	<input type="checkbox"/>	2		
191.5 ft.	Hole				0	<input type="checkbox"/>	7		3
192.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	10		
245.7 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	2		
260.3 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	10		
262.0 ft.	Water Level				5	<input type="checkbox"/>			
262.1 ft.	Tap Factory Made		8			<input type="checkbox"/>	6		
Remarks: drop line									
262.2 ft.	Infiltration Runner					<input checked="" type="checkbox"/>	8	10	4
Remarks: drop line									
262.3 ft.	Survey Abandoned				0	<input type="checkbox"/>			
Remarks: CAN NOT PASS DROPPED INVERT									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D19-8_D19-7	Oliver Springs	Sleepy Hollow	Concrete Pipe (non-...	Yard	Sanitary
Upstream MH D19-8	Total Length 262.2	Year Laid	Shape Circular	Location Details	
DS Manhole D19-7	Length surveyed 262.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4



Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D19-7(D19-8)



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

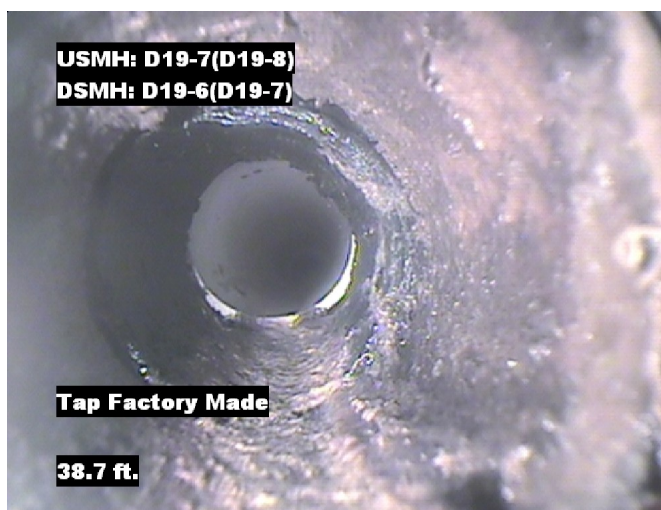

Distance: 38.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Distance: 68.3 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D19-8_D19-7	Oliver Springs	Sleepy Hollow	Concrete Pipe (non-...	Yard	Sanitary
Upstream MH D19-8	Total Length 262.2	Year Laid	Shape Circular	Location Details	
DS Manhole D19-7	Length surveyed 262.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4

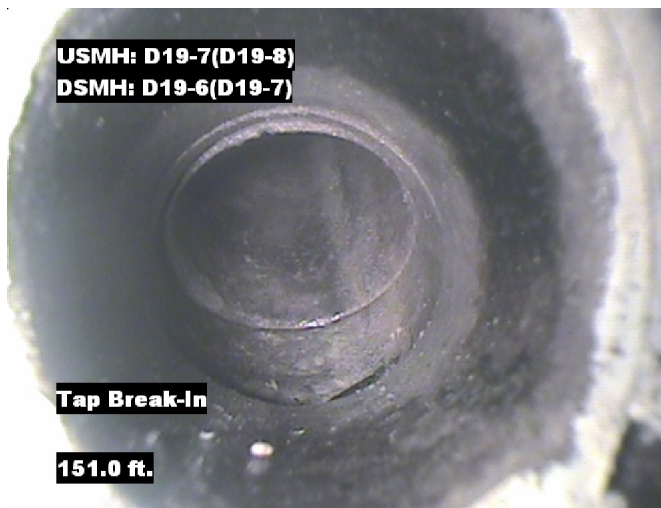

Distance: 151.0 ft. Grade: 0
Condition: Tap Break-In
Remarks: N/A

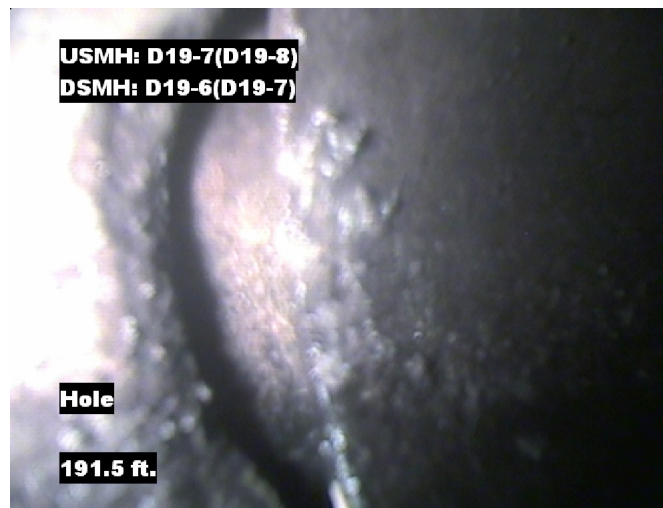

Distance: 191.5 ft. Grade: 3
Condition: Hole
Remarks: N/A



Distance: 192.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 245.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

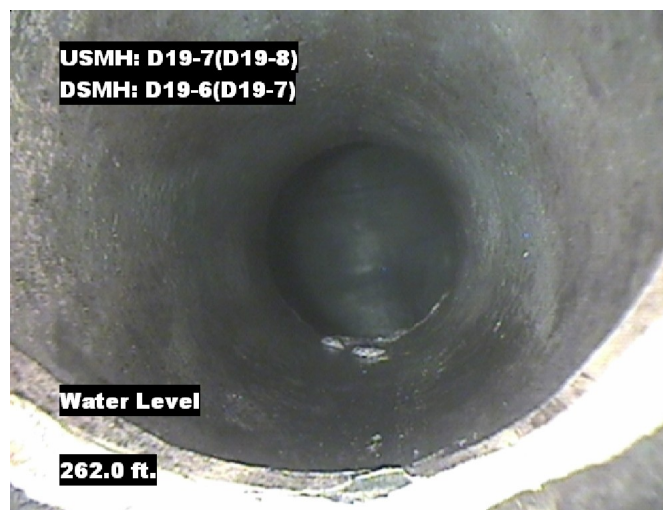


Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D19-8_D19-7	Oliver Springs	Sleepy Hollow	Concrete Pipe (non-...	Yard	Sanitary
Upstream MH D19-8	Total Length 262.2	Year Laid	Shape Circular	Location Details	
DS Manhole D19-7	Length surveyed 262.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4



Distance: 260.3 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 262.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 262.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: drop line



Distance: 262.2 ft. Grade: 4
Condition: Infiltration Runner
Remarks: drop line



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D19-8_D19-7	Oliver Springs	Sleepy Hollow	Concrete Pipe (non-...	Yard	Sanitary
Upstream MH D19-8	Total Length 262.2	Year Laid	Shape Circular	Location Details	
DS Manhole D19-7	Length surveyed 262.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4



Distance: 262.3 ft. Grade: 0
Condition: Survey Abandoned
Remarks: CAN NOT PASS DROPPED INVERT



Pipe Segment Refere... D19-8_D19-7	City Oliver Springs	Street Sleepy Hollow	Material Concrete Pipe (non-...		Location C... Yard	Sewer Use Sanitary
Upstream MH D19-8	Total Length 262.2	Year Laid	Shape Circular		Location Details	
DS Manhole D19-7	Length surveyed 262.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4	
SPR 3	MPR 4	PO Number 4397-03		Customer GRW		
SPRI 3	MPRI 4	Work Order 4397-02		Purpose		
QSR 3100	QMR 4100			Pre-Rehabilitation Survey		
OPR 7	Surveyed By Barry_Rogers	Direction Downstream	Date 20150630		Media label	
OPRI 3.5	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 08:13		Weather Damp	
Date Cleaned 20150630			End Time 08:43		Additional Info	

Page #: 6
