



Defect Listing

Pipe Segment Refere... D6-3_D6-2	City Oliver Springs	Street Dale St	Material Concrete Pipe (non-...	Location C... Yard	Sewer Use Sanitary
Upstream MH D6-3	Total Length 288.2	Year Laid	Shape Circular	Location Details	
DS Manhole D6-2	Length surveyed 288.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4


SPR N/A	MPR 5	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 5	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 5100		
OPR 5	Surveyed By Barry Rogers	Direction Downstream	Date 20150706
OPRI 5	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 13:07
	Date Cleaned 20150706	End Time 13:20	Weather Dry
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D6-3									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
177.3 ft.	Tap Factory Made Active		6		0	<input type="checkbox"/>	12		
262.8 ft.	Infiltration Gusher				0	<input checked="" type="checkbox"/>	1	12	5
284.5 ft.	Water Level				15	<input type="checkbox"/>			
288.2 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D6-2									




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D6-3_D6-2	Oliver Springs	Dale St	Concrete Pipe (non-...	Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D6-3	288.2		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D6-2	288.2		8	8	4

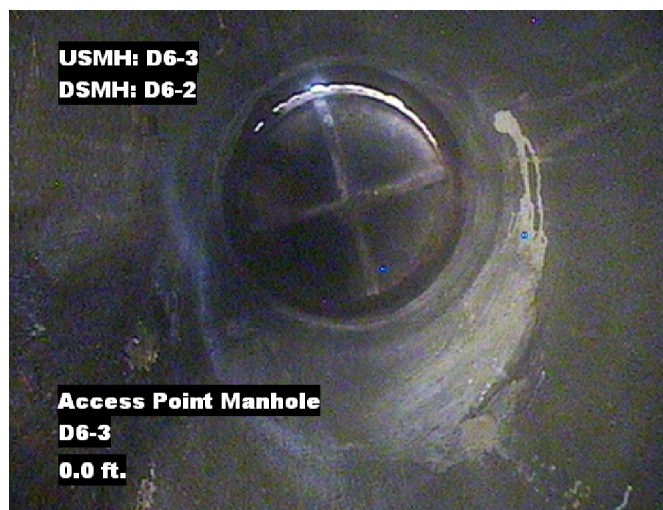


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D6-3

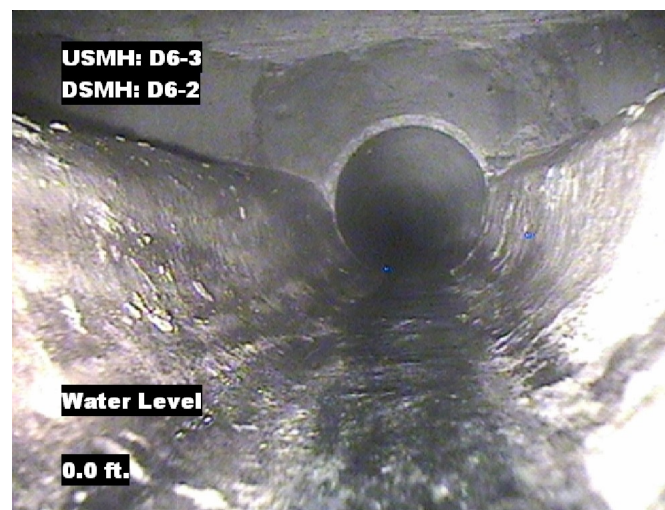

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 177.3 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A

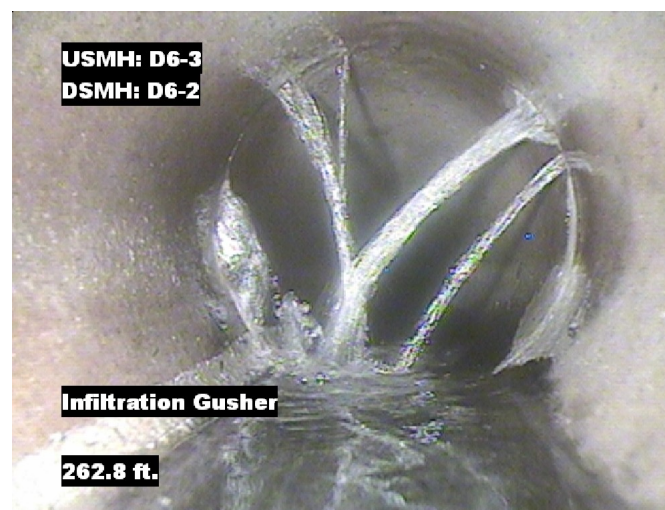

Distance: 262.8 ft. Grade: 5
Condition: Infiltration Gusher
Remarks: N/A

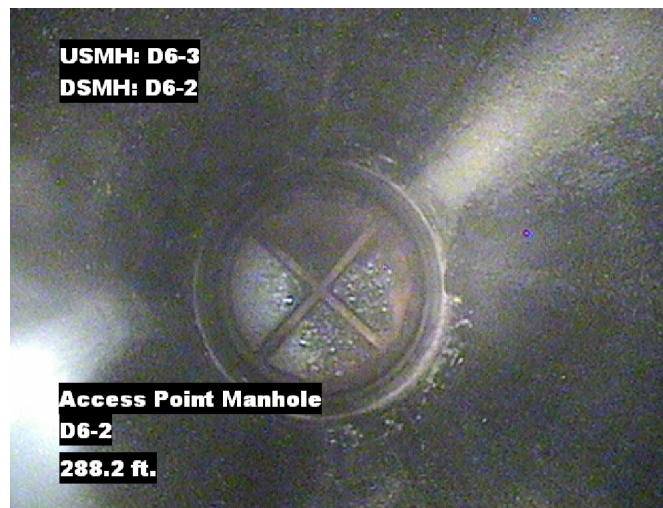


Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D6-3_D6-2	Oliver Springs	Dale St	Concrete Pipe (non-...	Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D6-3	288.2		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D6-2	288.2		8	8	4



Distance: 284.5 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 288.2 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D6-2



PACP Conditions

Pipe Segment Refere... D6-3_D6-2	City Oliver Springs	Street Dale St	Material Concrete Pipe (non-...	Location C... Yard	Sewer Use Sanitary
Upstream MH D6-3	Total Length 288.2	Year Laid	Shape Circular	Location Details	
DS Manhole D6-2	Length surveyed 288.2	Year Renewed	Height 8	Width 8	Pipe Joint... 4

SPR N/A	MPR 5	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 5	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 5100		
OPR 5	Surveyed By Barry Rogers	Direction Downstream	Date 20150706
OPRI 5	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 13:07
	Date Cleaned 20150706	End Time 13:20	Weather Dry
		Additional Info	

Normal Defects			Structural Ratings		O & M Ratings			Combined Ratings			
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	1	5	5	1	5
Code	ID	Length									
