



Defect Listing

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D6-5_D6-4	Oliver Springs	Dale St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D6-5	373.9		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D6-4	373.9		8	8	4


SPR	5	MPR	N/A	PO Number	Customer
SPRI	2.5	MPRI	N/A	4397-03	GRW
QSR	4111	QMR	N/A	Work Order	Purpose
				4397-02	Pre-Rehabilitation Survey
OPR		Surveyed By	Direction	Date	Media label
5		Barry Rogers	Downstream	20150706	
OPRI		Certificate Number	Pre-Cleaning	Time	Weather
2.5		U-1012-16405	Jetting	09:58	Dry
Date Cleaned				End Time	Additional Info
20150706				10:21	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D6-5									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
67.8 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
191.2 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
244.7 ft.	Broken Pipe				0	<input type="checkbox"/>	10	12	4
298.5 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
353.1 ft.	Joint Offset Medium				0	<input type="checkbox"/>			1
371.3 ft.	Water Level				5	<input type="checkbox"/>			
373.9 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D6-4									




Image Report 4/Page


Pipe Segment Refere... D6-5_D6-4	City Oliver Springs	Street Dale St	Material Concrete Pipe (non-...		Location C... Light High...	Sewer Use Sanitary
Upstream MH D6-5	Total Length 373.9	Year Laid	Shape Circular		Location Details	
DS Manhole D6-4	Length surveyed 373.9	Year Renewed	Height 8	Width 8	Pipe Joint... 4	

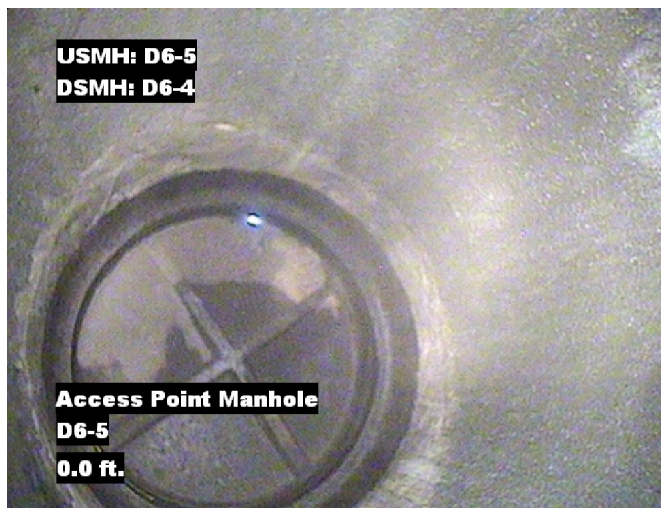

Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D6-5

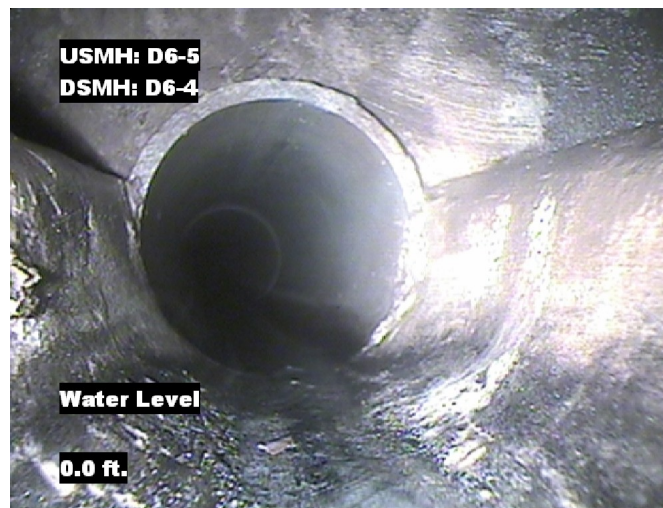

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

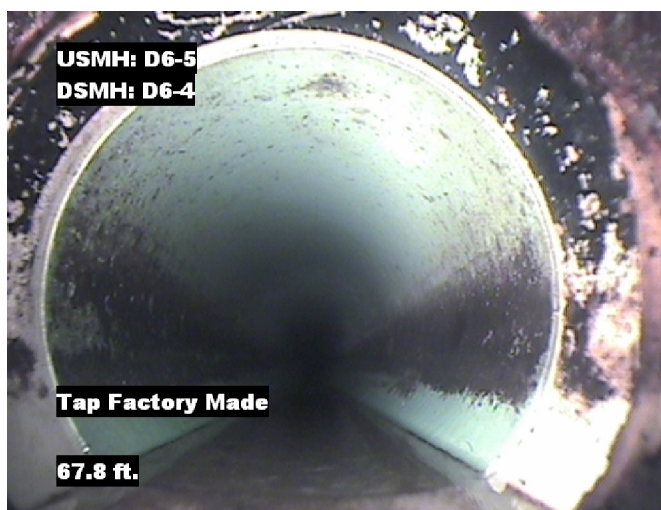

Distance: 67.8 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Distance: 191.2 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D6-5_D6-4	Oliver Springs	Dale St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D6-5	373.9		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D6-4	373.9		8	8	4

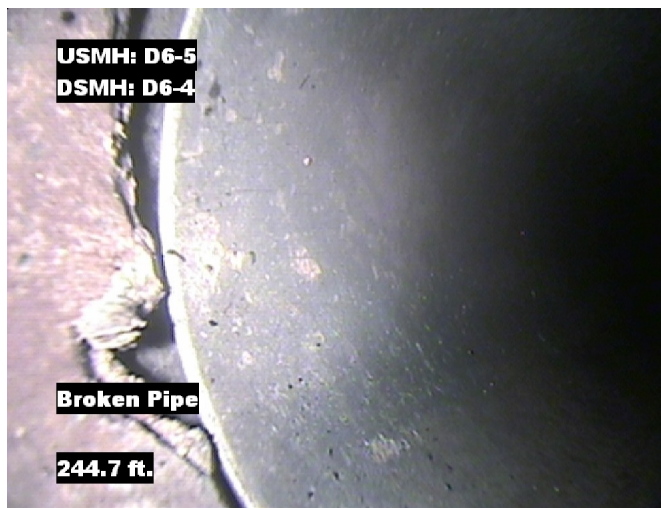

Distance: 244.7 ft. Grade: 4
Condition: Broken Pipe
Remarks: N/A

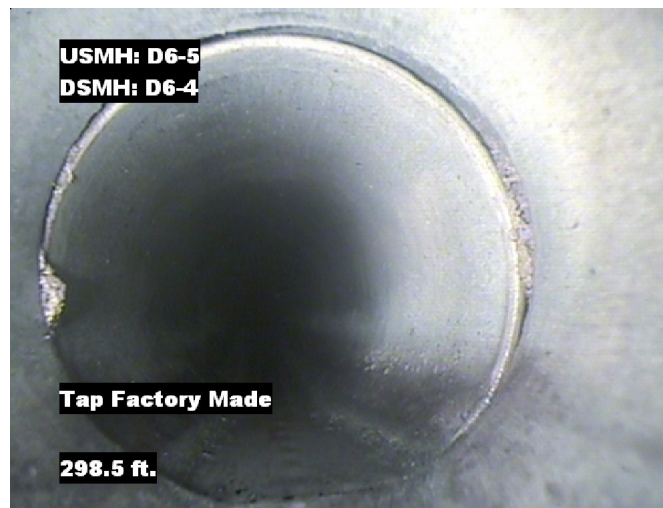

Distance: 298.5 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

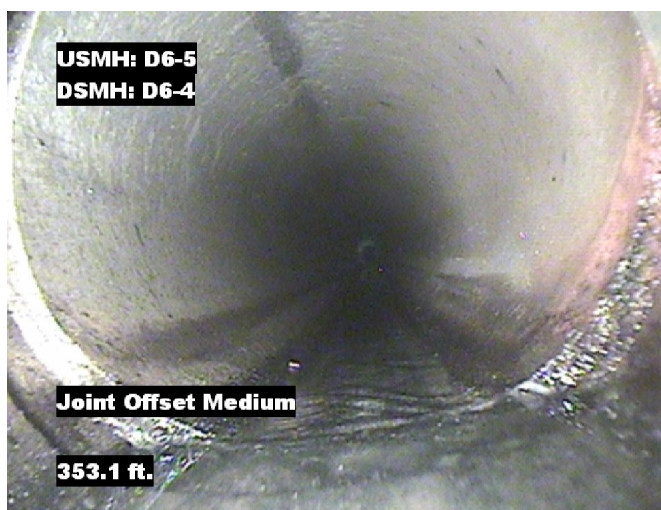

Distance: 353.1 ft. Grade: 1
Condition: Joint Offset Medium
Remarks: N/A



Distance: 371.3 ft. Grade: 0
Condition: Water Level
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D6-5_D6-4	Oliver Springs	Dale St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D6-5	373.9		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D6-4	373.9		8	8	4



Distance: 373.9 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D6-4



PACP Conditions

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D6-5_D6-4	Oliver Springs	Dale St	Concrete Pipe (non-...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D6-5	373.9		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D6-4	373.9		8	8	4
SPR	5	MPR	N/A	Customer	
SPRI	2.5	MPRI	N/A	GRW	
QSR	4111	QMR	N/A	Purpose	
				Pre-Rehabilitation Survey	
OPR	Surveyed By	Direction	Date	Media label	
5	Barry_Rogers	Downstream	20150706		
OPRI	Certificate Number	Pre-Cleaning	Time	Weather	
2.5	U-1012-16405	Jetting	09:58	Dry	
Date Cleaned			End Time	Additional Info	
20150706			10:21		

[illegible]
