



Defect Listing

Pipe Segment Refere... D9-1_D-16	City Oliver Springs	Street Midway Dr	Material Fibreglass Reinforc...	Location C... Light High...	Sewer Use Sanitary
Upstream MH D9-1	Total Length 354.4	Year Laid	Shape Circular	Location Details	
DS Manhole D-16	Length surveyed 354.4	Year Renewed	Height 10	Width 10	Pipe Joint... N/A


SPR N/A	MPR 8	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 2	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 2400		
OPR 8	Surveyed By Barry Rogers	Direction Downstream	Date 20150703
OPRI 2	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 07:50
	Date Cleaned 20150703	End Time 08:13	Weather Damp
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D9-1									
0.0 ft.	Water Level				30	<input type="checkbox"/>			
9.8 ft.	Deposits Attached Grease	S01			5	<input type="checkbox"/>	3	9	2
32.3 ft.	Deposits Attached Grease	F01			5	<input type="checkbox"/>	3	9	2
63.9 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	10		
140.8 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
143.6 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
184.4 ft.	Tap Factory Made Active		6		0	<input type="checkbox"/>	2		
241.0 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
269.5 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
354.0 ft.	Water Level				5	<input type="checkbox"/>			
354.4 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: D-16									



Image Report 4/Page


Pipe Segment Refere... D9-1_D-16	City Oliver Springs	Street Midway Dr	Material Fibreglass Reinforc...		Location C... Light High...	Sewer Use Sanitary
Upstream MH D9-1	Total Length 354.4	Year Laid	Shape Circular		Location Details	
DS Manhole D-16	Length surveyed 354.4	Year Renewed	Height 10	Width 10	Pipe Joint...	
					N/A	

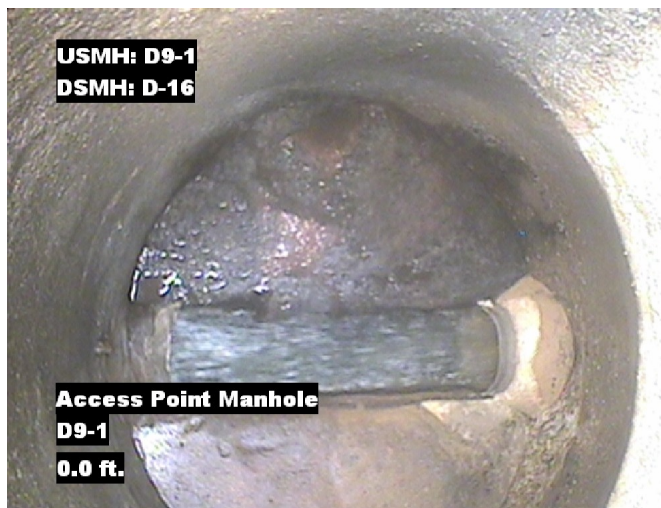

Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D9-1



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

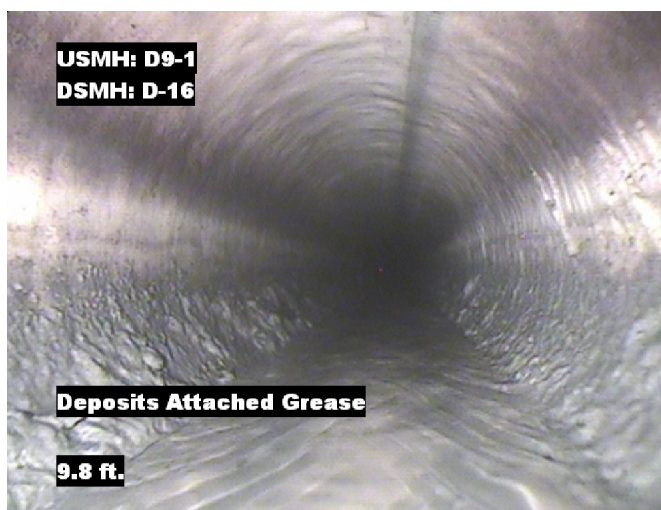

Distance: 9.8 ft. Grade: 2
Condition: Deposits Attached Grease
Remarks: N/A




Distance: 32.3 ft. Grade: 2
Condition: Deposits Attached Grease
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D9-1_D-16	Oliver Springs	Midway Dr	Fibreglass Reinforc...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D9-1	354.4		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D-16	354.4		10	10	N/A

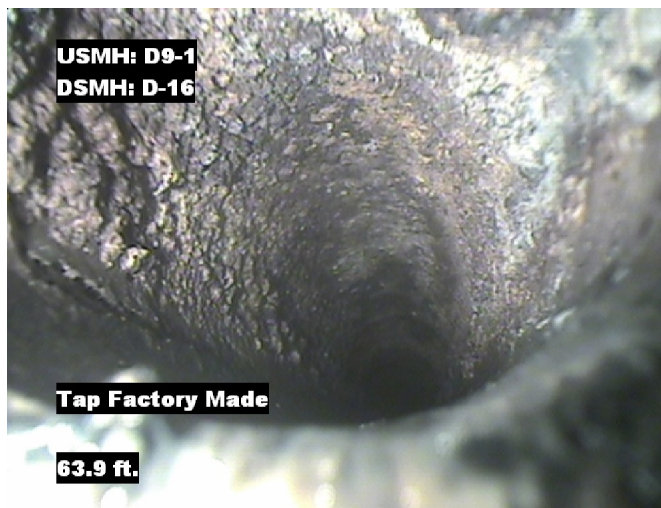


Distance: 63.9 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

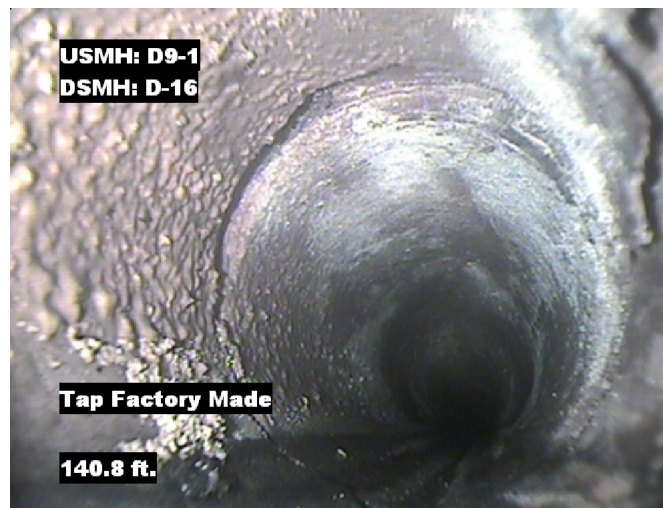

Distance: 140.8 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

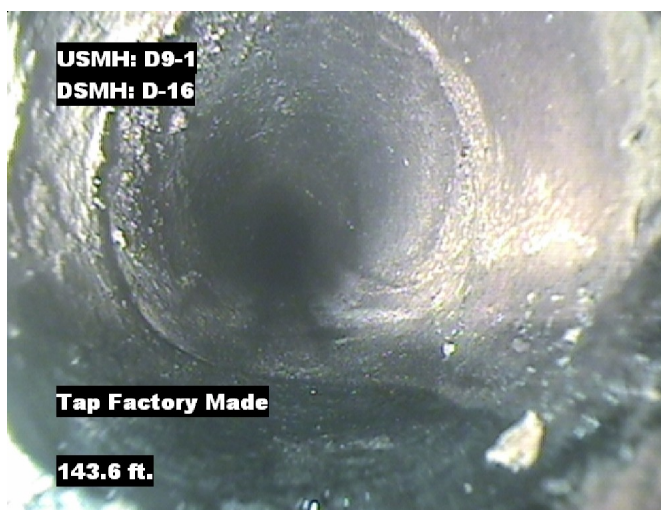

Distance: 143.6 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

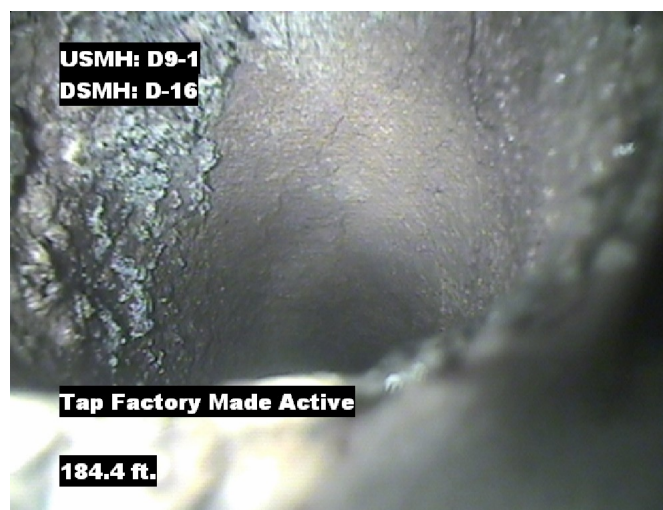


Distance: 184.4 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
D9-1_D-16	Oliver Springs	Midway Dr	Fibreglass Reinforc...	Light High...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
D9-1	354.4		Circular		
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
D-16	354.4		10	10	N/A

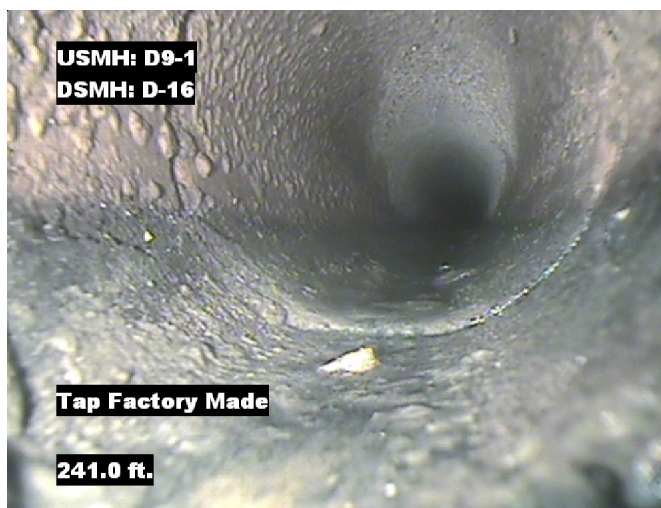

Distance: 241.0 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

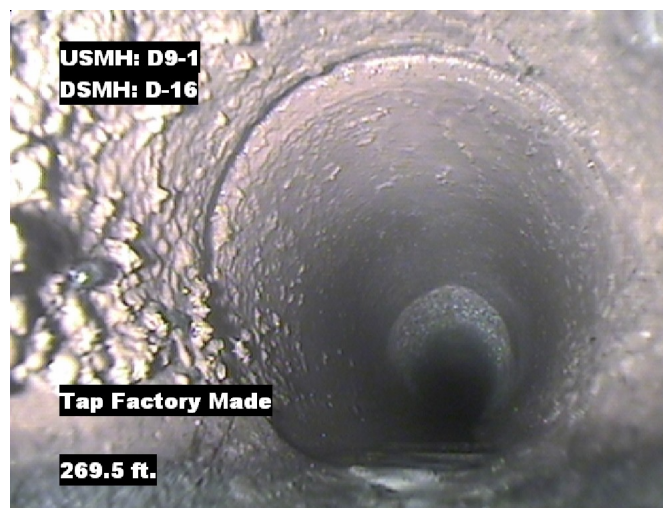

Distance: 269.5 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

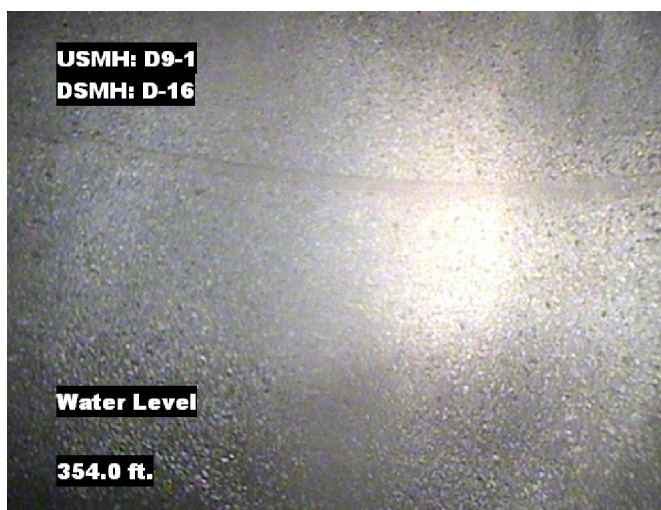

Distance: 354.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 354.4 ft. Grade: 0
Condition: Access Point Manhole
Remarks: D-16



PACP Conditions

Pipe Segment Refere... D9-1_D-16	City Oliver Springs	Street Midway Dr	Material Fibreglass Reinforc...	Location C... Light High...	Sewer Use Sanitary
Upstream MH D9-1	Total Length 354.4	Year Laid	Shape Circular	Location Details	
DS Manhole D-16	Length surveyed 354.4	Year Renewed	Height 10	Width 10	Pipe Joint... N/A
SPR N/A	MPR 8	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI 2	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR 2400				
OPR 8	Surveyed By Barry Rogers	Direction Downstream	Date 20150703	Media label	
OPRI 2	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 07:50	Weather Damp	
Date Cleaned 20150703			End Time 08:13	Additional Info	

Normal Defects			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	0	0	2	0	0
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Code	ID	Length	0	0	0	2	4	8	2	4	8
DAGS	F01	22.5									
			Subtotals	0		Subtotals	4		Subtotals	4	
SUMMARY			Pipe Rating	0		Pipe Rating	8		Overall Pipe Rating	8	
			Structural Index	0		O&M Index	2.0		Overall Index	2.0	
			Str. Quick Rating	0000		O&M Quick Rating	2400		Ovrl. Quick Rating	2400	
