



Defect Listing

Pipe Segment Refere... E-12A_E-12B	City Oliver Springs	Street 761 Sleepy Hollow	Material PolyVinyl Chloride	Location C... Yard	Sewer Use Sanitary
Upstream MH E-12A	Total Length 135.7	Year Laid	Shape Circular	Location Details Front Yard	
DS Manhole E-12B	Length surveyed 135.7	Year Renewed	Height 8	Width 8	Pipe Joint... 13


SPR 81	MPR 2	PO Number 4397-03	Customer GRW
SPRI 3	MPRI 2	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR 3D00	QMR 2100		
OPR 83	Surveyed By Barry Rogers	Direction Downstream	Date 20150608
OPRI 3	Certificate Number U-1012-16405	Pre-Cleaning No Pre-Cleaning	Time 12:44
	Date Cleaned	End Time 12:52	Weather Dry
		Additional Info	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E-12A									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
0.0 ft.	Surface Aggregate Visible	S01			0	<input type="checkbox"/>	3	9	3
60.4 ft.	Tap Break-In		6		0	<input type="checkbox"/>	2		
76.9 ft.	Tap Break-In		6		0	<input type="checkbox"/>	10		
130.7 ft.	Water Level				15	<input type="checkbox"/>			
132.5 ft.	Deposits Attached Grease				5	<input type="checkbox"/>	3	9	2
134.9 ft.	Water Level				10	<input type="checkbox"/>			
135.0 ft.	Surface Aggregate Visible	F01			0	<input type="checkbox"/>	3	9	3
135.7 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E-12B									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E-12A_E-12B	Oliver Springs	761 Sleepy Hollow	PolyVinyl Chloride	Yard	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
E-12A	135.7		Circular	Front Yard	
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
E-12B	135.7		8	8	13

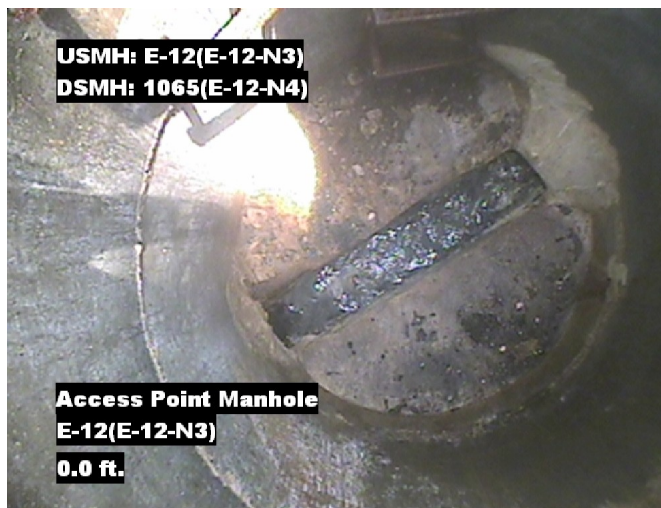


Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E-12A



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

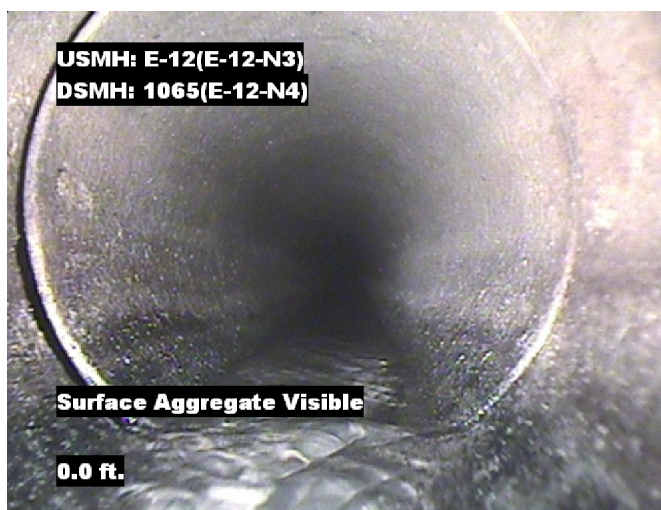

Distance: 0.0 ft. Grade: 3
Condition: Surface Aggregate Visible
Remarks: N/A

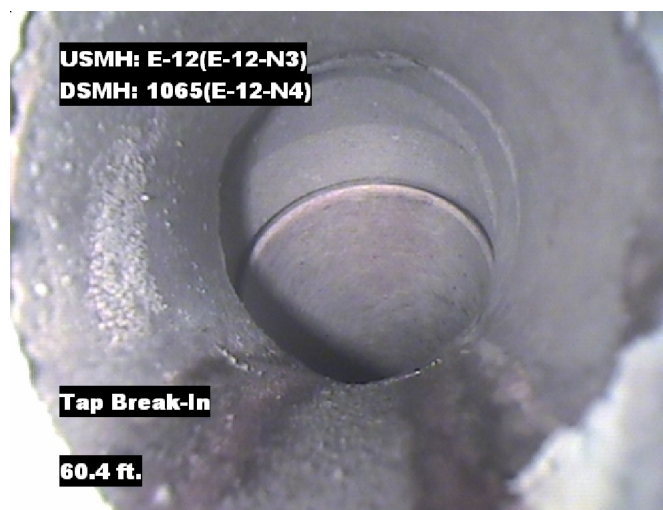


Distance: 60.4 ft. Grade: 0
Condition: Tap Break-In
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E-12A_E-12B	Oliver Springs	761 Sleepy Hollow	PolyVinyl Chloride	Yard	Sanitary
Upstream MH E-12A	Total Length 135.7	Year Laid	Shape Circular	Location Details Front Yard	
DS Manhole E-12B	Length surveyed 135.7	Year Renewed	Height 8	Width 8	Pipe Joint... 13

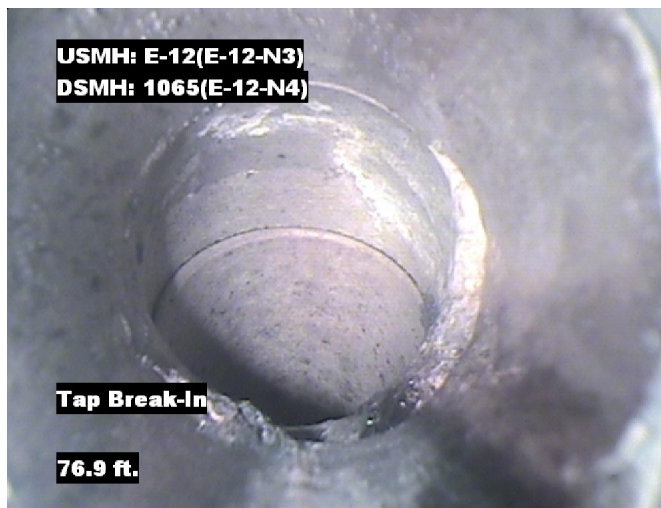

Distance: 76.9 ft. Grade: 0
Condition: Tap Break-In
Remarks: N/A



Distance: 130.7 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 132.5 ft. Grade: 2
Condition: Deposits Attached Grease
Remarks: N/A




Distance: 134.9 ft. Grade: 0
Condition: Water Level
Remarks: N/A




Image Report 4/Page

Pipe Segment Refere... E-12A_E-12B	City Oliver Springs	Street 761 Sleepy Hollow	Material PolyVinyl Chloride		Location C... Yard	Sewer Use Sanitary
Upstream MH E-12A	Total Length 135.7	Year Laid	Shape Circular		Location Details Front Yard	
DS Manhole E-12B	Length surveyed 135.7	Year Renewed	Height 8	Width 8	Pipe Joint... 13	

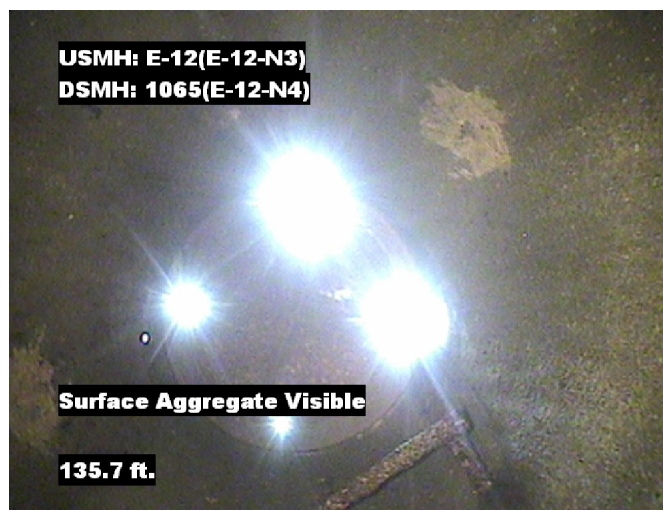

Distance: 135.0 ft. Grade: 3
Condition: Surface Aggregate Visible
Remarks: N/A

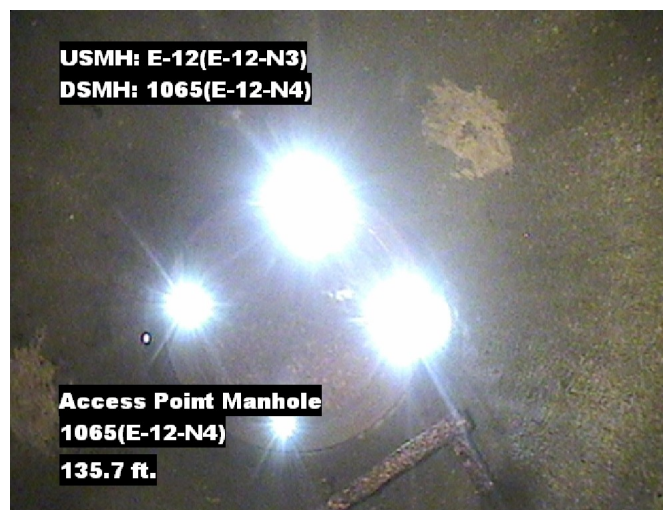

Distance: 135.7 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E-12B



PACP Conditions

Pipe Segment Refere... E-12A_E-12B	City Oliver Springs	Street 761 Sleepy Hollow	Material PolyVinyl Chloride	Location C... Yard	Sewer Use Sanitary
Upstream MH E-12A	Total Length 135.7	Year Laid	Shape Circular	Location Details Front Yard	
DS Manhole E-12B	Length surveyed 135.7	Year Renewed	Height 8	Width 8	Pipe Joint... 13
SPR 81	MPR 2	PO Number 4397-03		Customer GRW	
SPRI 3	MPRI 2	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR 3D00	QMR 2100	Direction Downstream		Date 20150608	
OPR 83	Surveyed By Barry Rogers	Pre-Cleaning No Pre-Cleaning		Media label	
OPRI 3	Certificate Number U-1012-16405	Time 12:44		Weather Dry	
Date Cleaned			End Time 12:52		Additional Info

Normal Defects			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Continuous Defects			1	0	0	1	0	0	1	0	0
			2	0	0	2	1	2	2	1	2
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Code	ID	Length	3	27	81	0	0	0	3	27	81
SAV	F01	135.0									
			Subtotals	27		Subtotals	1		Subtotals	28	
SUMMARY			Pipe Rating		81	Pipe Rating		2	Overall Pipe Rating		83
			Structural Index		3.0	O&M Index		2.0	Overall Index		3.0
			Str. Quick Rating		3D00	O&M Quick Rating		2100	Ovrl. Quick Rating		3D21
