



Defect Listing

Pipe Segment Refere... E-15_E-14	City Oliver Springs	Street Cedar Ln	Material PolyVinyl Chloride	Location C... Easement/R...	Sewer Use Sanitary
Upstream MH E-15	Total Length 188.2	Year Laid	Shape Circular	Location Details Side of Rd	
DS Manhole E-14	Length surveyed 188.2	Year Renewed	Height 8	Width 8	Pipe Joint... 13

SPR N/A	MPR 6	PO Number 4397-03	Customer GRW
SPRI N/A	MPRI 3	Work Order 4397-02	Purpose Pre-Rehabilitation Survey
QSR N/A	QMR 4121		
OPR 6	Surveyed By Barry Rogers	Direction Downstream	Date 20150605
OPRI 3	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 14:41
	Date Cleaned 20150605	End Time 14:53	Weather Dry
			Media label
			Additional Info

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E-15									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
112.4 ft.	Tap Factory Made Active		6		0	<input checked="" type="checkbox"/>	9		
127.6 ft.	Water Level Sag				20	<input type="checkbox"/>			2
178.0 ft.	Camera Underwater				0	<input type="checkbox"/>			4
188.0 ft.	Water Level				10	<input type="checkbox"/>			
188.2 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E-14									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E-15_E-14	Oliver Springs	Cedar Ln	PolyVinyl Chloride	Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
E-15	188.2		Circular	Side of Rd	
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
E-14	188.2		8	8	13



Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E-15



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

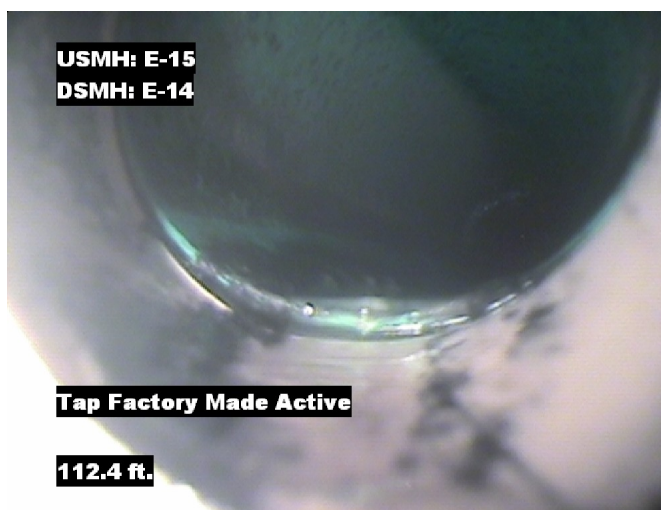

Distance: 112.4 ft. Grade: 0
Condition: Tap Factory Made Active
Remarks: N/A




Distance: 127.6 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material		Location C...	Sewer Use
E-15_E-14	Oliver Springs	Cedar Ln	PolyVinyl Chloride		Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape		Location Details	
E-15	188.2		Circular		Side of Rd	
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...	
E-14	188.2		8	8	13	

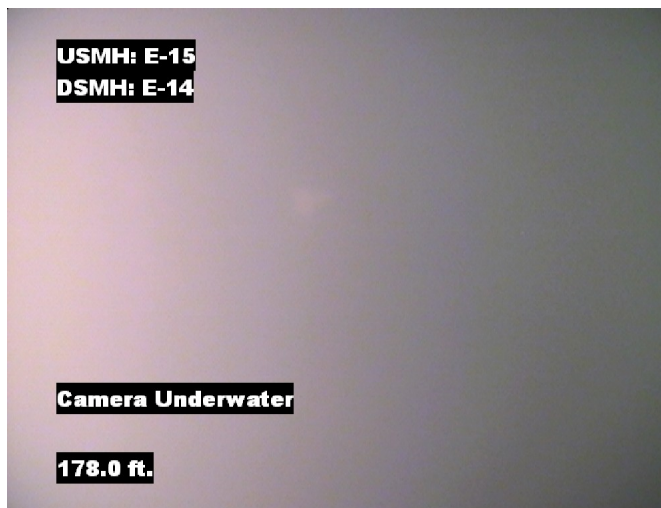

Distance: 178.0 ft. Grade: 4
Condition: Camera Underwater
Remarks: N/A



Distance: 188.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 188.2 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E-14



PACP Conditions

Pipe Segment Refere... E-15_E-14	City Oliver Springs	Street Cedar Ln	Material PolyVinyl Chloride	Location C... Easement/R...	Sewer Use Sanitary
Upstream MH E-15	Total Length 188.2	Year Laid	Shape Circular	Location Details Side of Rd	
DS Manhole E-14	Length surveyed 188.2	Year Renewed	Height 8	Width 8	Pipe Joint... 13
SPR N/A	MPR 6	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI 3	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR 4121				
OPR 6	Surveyed By Barry Rogers	Direction Downstream	Date 20150605	Media label	
OPRI 3	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 14:41	Weather Dry	
Date Cleaned 20150605			End Time 14:53	Additional Info	

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
			1	0	0	1	0	0	1	0	0
			2	0	0	2	1	2	2	1	2
			3	0	0	3	0	0	3	0	0
			4	0	0	4	1	4	4	1	4
			5	0	0	5	0	0	5	0	0
Continuous Defects											
Code	ID	Length									
