



Defect Listing

Pipe Segment Refere... E15-2 E15-2A	City Oliver Springs	Street Sleepy Hollow	Material PolyVinyl Chloride	Location C... Easement/R...	Sewer Use Sanitary
Upstream MH E15-2	Total Length 347.4	Year Laid	Shape Circular	Location Details Behind Houses	
DS Manhole E15-2A	Length surveyed 347.4	Year Renewed	Height 8	Width 8	Pipe Joint... 13


SPR N/A	MPR 44	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI 2	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR 2C00				
OPR 44	Surveyed By Barry Rogers	Direction Downstream	Date 20150605	Media label	
OPRI 2	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 09:22	Weather Dry	
Date Cleaned 20150605			End Time 09:49	Additional Info Manholes are Not La...	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E15-2									
0.0 ft.	Water Level				5	<input type="checkbox"/>			
24.7 ft.	Tap Factory Made		6		0	<input checked="" type="checkbox"/>	9		
112.8 ft.	Tap Factory Made		6		0	<input checked="" type="checkbox"/>	9		
213.1 ft.	Tap Factory Made		6		0	<input checked="" type="checkbox"/>	9		
256.2 ft.	Water Level Sag	S01			20	<input type="checkbox"/>			2
285.1 ft.	Water Level				10	<input type="checkbox"/>			
314.2 ft.	Tap Break-In Intruding		6	1	0	<input checked="" type="checkbox"/>	9		2
330.9 ft.	Water Level Sag	S02			20	<input type="checkbox"/>			2
347.2 ft.	Water Level				10	<input type="checkbox"/>			
347.4 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E15-2A									
347.4 ft.	Water Level Sag	F02			20	<input type="checkbox"/>			2
347.4 ft.	Water Level Sag	F01			20	<input type="checkbox"/>			2




Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E15-2 E15-2A	Oliver Springs	Sleepy Hollow	PolyVinyl Chloride	Easement/R...	Sanitary
Upstream MH E15-2	Total Length 347.4	Year Laid	Shape Circular	Location Details Behind Houses	
DS Manhole E15-2A	Length surveyed 347.4	Year Renewed	Height 8	Width 8	Pipe Joint... 13

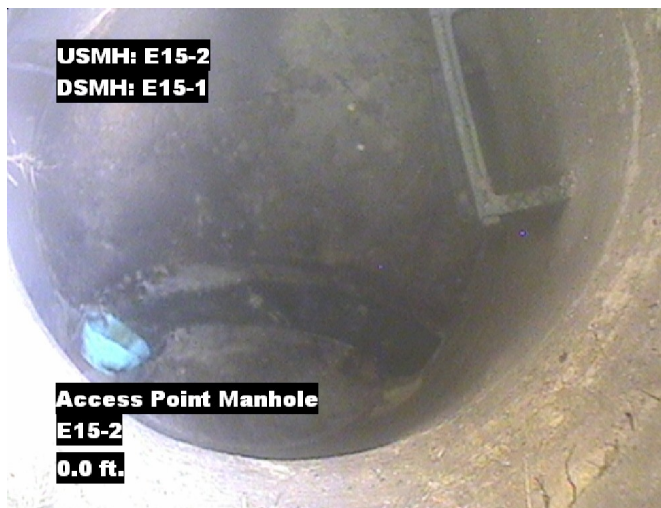

Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E15-2

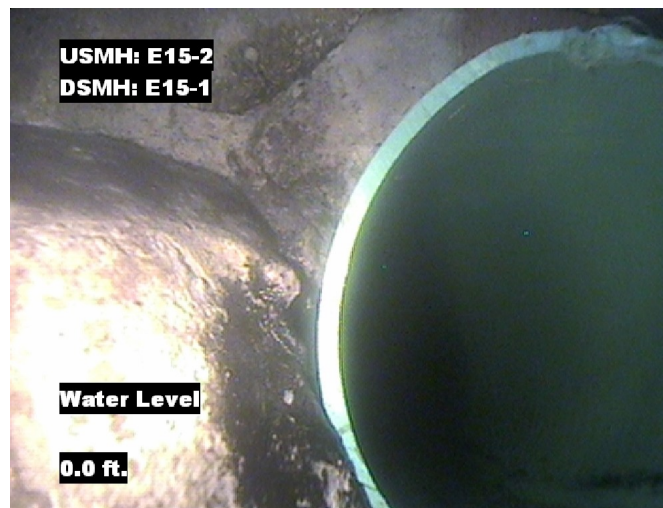

Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

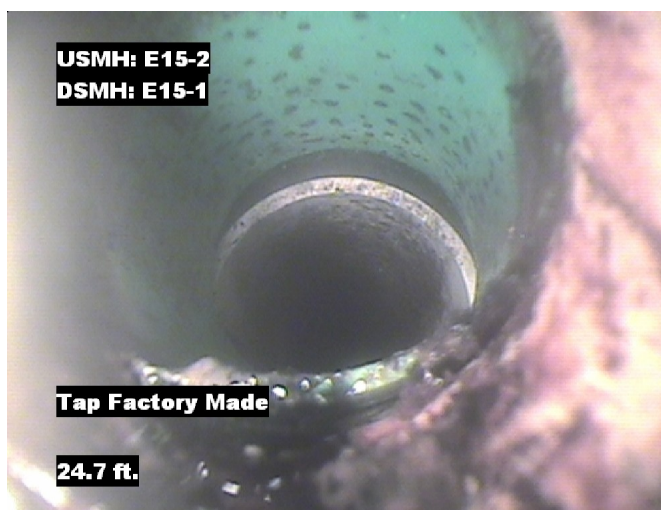

Distance: 24.7 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 112.8 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E15-2_E15-2A	Oliver Springs	Sleepy Hollow	PolyVinyl Chloride	Easement/R...	Sanitary
Upstream MH E15-2	Total Length 347.4	Year Laid	Shape Circular	Location Details Behind Houses	
DS Manhole E15-2A	Length surveyed 347.4	Year Renewed	Height 8	Width 8	Pipe Joint... 13




Distance: 213.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 256.2 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A



Distance: 285.1 ft. Grade: 0
Condition: Water Level
Remarks: N/A

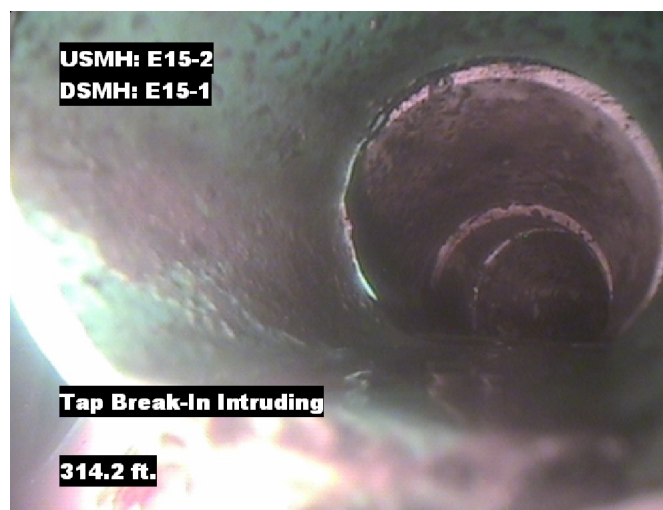


Distance: 314.2 ft. Grade: 2
Condition: Tap Break-In Intruding
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E15-2 E15-2A	Oliver Springs	Sleepy Hollow	PolyVinyl Chloride	Easement/R...	Sanitary
Upstream MH E15-2	Total Length 347.4	Year Laid	Shape Circular	Location Details Behind Houses	
DS Manhole E15-2A	Length surveyed 347.4	Year Renewed	Height 8	Width 8	Pipe Joint... 13

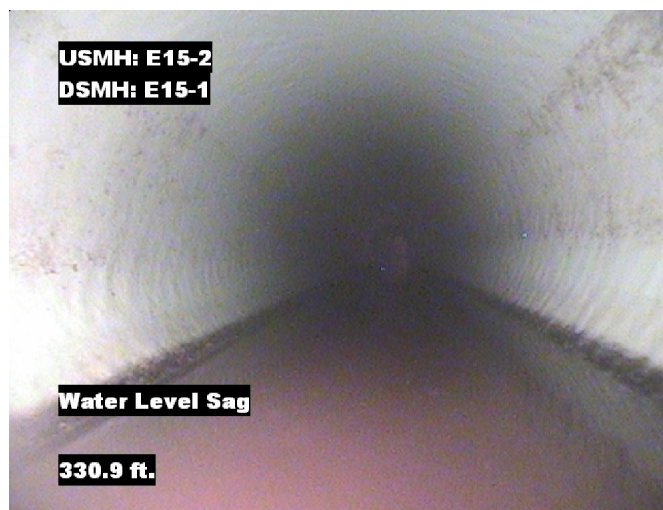

Distance: 330.9 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A



Distance: 347.2 ft. Grade: 0
Condition: Water Level
Remarks: N/A



Distance: 347.4 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E15-2A



Distance: 347.4 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A



Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E15-2_E15-2A	Oliver Springs	Sleepy Hollow	PolyVinyl Chloride	Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
E15-2	347.4		Circular	Behind Houses	
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
E15-2A	347.4		8	8	13



Distance: 347.4 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A



Pipe Segment Refere... E15-2_E15-2A	City Oliver Springs	Street Sleepy Hollow	Material PolyVinyl Chloride		Location C... Easement/R...	Sewer Use Sanitary
Upstream MH E15-2	Total Length 347.4	Year Laid	Shape Circular		Location Details Behind Houses	
DS Manhole E15-2A	Length surveyed 347.4	Year Renewed	Height 8	Width 8	Pipe Joint... 13	
SPR N/A	MPR 44	PO Number 4397-03		Customer GRW		
SPRI N/A	MPRI 2	Work Order 4397-02		Purpose Pre-Rehabilitation Survey		
QSR N/A	QMR 2C00					
OPR 44	Surveyed By Barry_Rogers	Direction Downstream	Date 20150605		Media label	
OPRI 2	Certificate Number U-1012-16405	Pre-Cleaning Jetting	Time 09:22		Weather Dry	
Date Cleaned 20150605		End Time 09:49		Additional Info Manholes are Not La...		

Page #: 6
