



Defect Listing

Pipe Segment Refere... E6-1_E4-3	City Oliver Springs	Street Easement	Material Other	Location C... Easement/R...	Sewer Use Sanitary
Upstream MH E6-1	Total Length 158.8	Year Laid	Shape Circular	Location Details Runs from Gail Ln t...	
DS Manhole E4-3	Length surveyed 158.8	Year Renewed	Height 8	Width 8	Pipe Joint... N/A

SPR N/A	MPR 2	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI 2	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR 2100				
OPR 2	Surveyed By Barry Rogers	Direction Downstream	Date 20150617	Media label	
OPRI 2	Certificate Number U-1012-16405	Pre-Cleaning Heavy Cleaning	Time 14:29	Weather Very Dry	
Date Cleaned 20150617			End Time 14:38	Additional Info	

Distance	Condition	Cont. Dfct.	Values			Joint	Clock Position		Grade
			1st	2nd	%		At/From	To	
0.0 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E6-1									
0.0 ft.	Water Level				10	<input type="checkbox"/>			
7.1 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	9		
62.5 ft.	Tap Factory Made		6		0	<input type="checkbox"/>	3		
152.7 ft.	Water Level Sag				20	<input type="checkbox"/>			2
158.8 ft.	Access Point Manhole				0	<input type="checkbox"/>			
Remarks: E4-3									



Image Report 4/Page


Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E6-1_E4-3	Oliver Springs	Easement	Other	Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
E6-1	158.8		Circular	Runs from Gail Ln t...	
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
E4-3	158.8		8	8	N/A



Distance: 0.0 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E6-1



Distance: 0.0 ft. Grade: 0
Condition: Water Level
Remarks: N/A

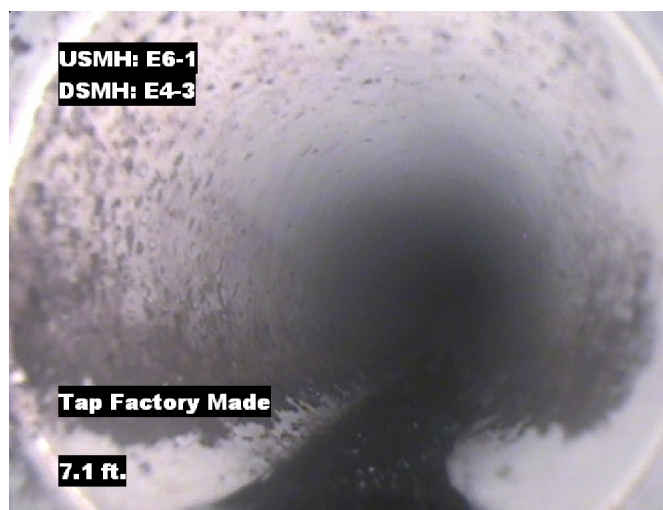

Distance: 7.1 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A



Distance: 62.5 ft. Grade: 0
Condition: Tap Factory Made
Remarks: N/A

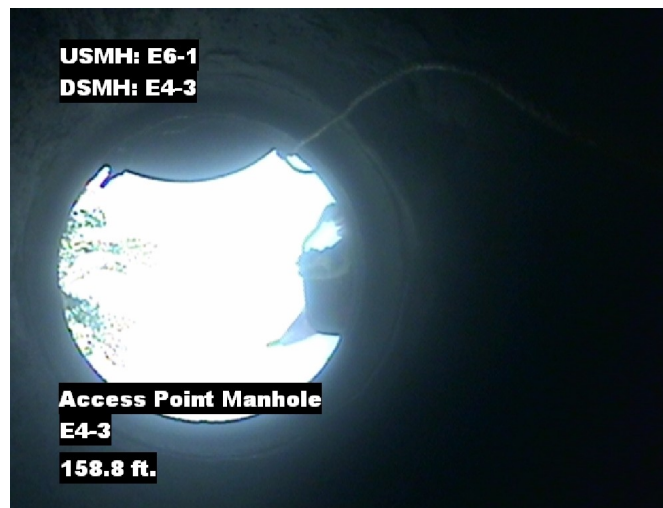


Image Report 4/Page

Pipe Segment Refere...	City	Street	Material	Location C...	Sewer Use
E6-1_E4-3	Oliver Springs	Easement	Other	Easement/R...	Sanitary
Upstream MH	Total Length	Year Laid	Shape	Location Details	
E6-1	158.8		Circular	Runs from Gail Ln t...	
DS Manhole	Length surveyed	Year Renewed	Height	Width	Pipe Joint...
E4-3	158.8		8	8	N/A



Distance: 152.7 ft. Grade: 2
Condition: Water Level Sag
Remarks: N/A



Distance: 158.8 ft. Grade: 0
Condition: Access Point Manhole
Remarks: E4-3



PACP Conditions

Pipe Segment Refere... E6-1_E4-3	City Oliver Springs	Street Easement	Material Other	Location C... Easement/R...	Sewer Use Sanitary
Upstream MH E6-1	Total Length 158.8	Year Laid	Shape Circular	Location Details Runs from Gail Ln t...	
DS Manhole E4-3	Length surveyed 158.8	Year Renewed	Height 8	Width 8	Pipe Joint... N/A
SPR N/A	MPR 2	PO Number 4397-03		Customer GRW	
SPRI N/A	MPRI 2	Work Order 4397-02		Purpose Pre-Rehabilitation Survey	
QSR N/A	QMR 2100	Direction Downstream		Date 20150617	
OPR 2	Surveyed By Barry Rogers	Pre-Cleaning Heavy Cleaning		Time 14:29	
OPRI 2	Certificate Number U-1012-16405	Date Cleaned 20150617		End Time 14:38	
			Media label		Weather Very Dry
			Additional Info		

			Structural Ratings			O & M Ratings			Combined Ratings		
			Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating	Grade Rating	No. Occur.	Rating
Normal Defects											
			1	0	0	1	0	0	1	0	0
			2	0	0	2	1	2	2	1	2
			3	0	0	3	0	0	3	0	0
			4	0	0	4	0	0	4	0	0
			5	0	0	5	0	0	5	0	0
Continuous Defects											
Code	ID	Length									
